

MANOKOTAK HEIGHTS ROAD RECONSTRUCTION

JUNE 3, 2014

PROJECT

INFORMATION:

Contractor

Ridge Contracting
Inc. (RCI)

Start Date


April 2013

Completion Date

Early Fall 2014

Construction

The Manokotak Heights Road Reconstruction project is shaping up! If you had the chance to travel through the work site you can see the slopes are coming close to completion. Turf establishment is starting to grow on all exposed slopes up to station 150+00.

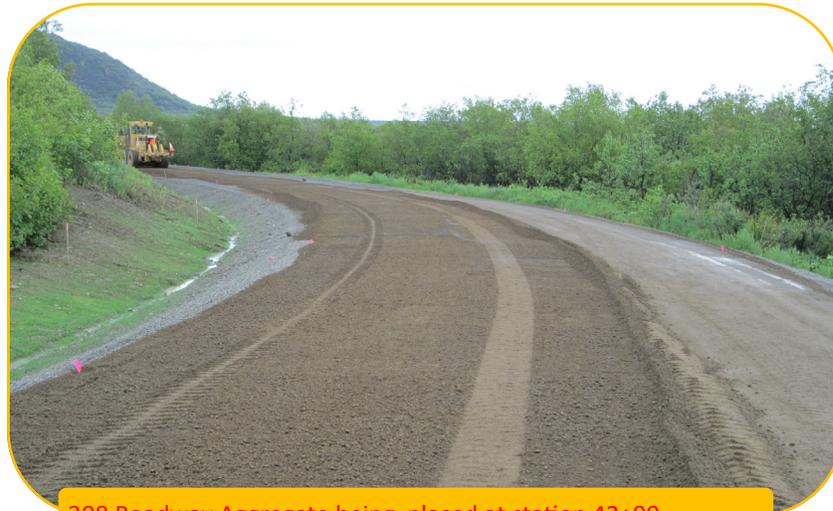

308 Roadway Aggregate being placed at station 42+00

- As always travelers should continue to expect delays of up to 30 minutes maximum to get passage through the work zone, please do not travel through the site without a pilot car escort.
- All community members wanting to conduct subsistence activities within the work zone such as , harvesting, berries, wild celery, or ferns, are asked to park in turnouts if possible and communicate with the pilot car driver where they will be at, then follow the pilot car out the work area when finished with the harvesting.
- If you are noticing pink feathers appearing on the roadway please do not run them over!

Please don't run them over!



Project News

2014 SEASON

- The majority of culverts are complete and only the 18" culvert installations in Manokotak Heights are left to do. When this culvert work starts you can expect similar traffic control using the pilot car.
- The major push from RCI is to build up the roadway. Currently 304 roadway aggregate is being placed on the surface in preparation for the calcium chloride treatment in the coming weeks.

WFLHD

Knud W. Martin
Project Engineer

knud.martin@dot.gov
(907) 500-8875



www.wfl.fhwa.dot.gov/projects/ak/manokotak/
