

Weekly Newsletter




July 1, 2016

Snug Harbor Road: Mile Post 0.0 to Mile Post 1.8

The separated bike path is progressing steadily down Snug Harbor Road. This past week Ancor, Inc. focused on excavating down to subgrade. Once subgrade was prepared geotextile fabric with areas of geogrid reinforcing were installed prior to placing select borrow material for the structure of the bike path. Select borrow has been placed for over half the length of the separated bike path.

Next week excavation work and bike path construction will continue. The crews will be going back and grading and compacting the bike path, in addition to cleaning up the side slopes. Installation of pipe culverts and driveway culverts will also begin next week. Residents along the bike path may experience short periods of disturbance to their driveways.

Construction operations this upcoming week will be 7:00 a.m. to 7:00 p.m. Tuesday through Friday. No work will be conducted on the project from Thursday evening, June 30th, through Monday, July 4th over the Independence Day Weekend. Have a great 4th of July!

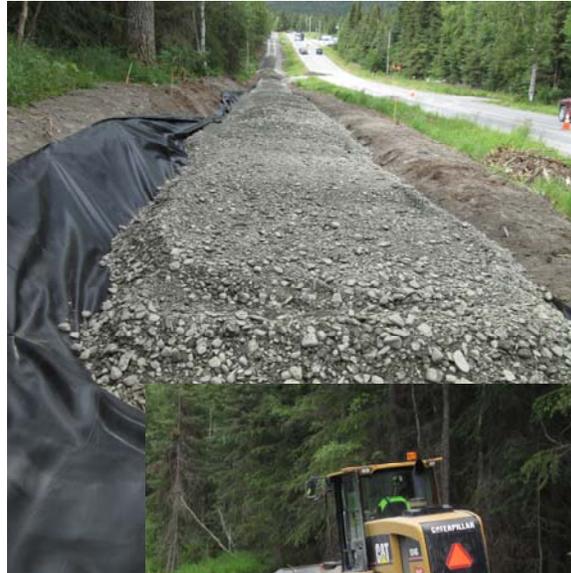

Ancor, Inc. constructing the separated bike path. Geotextile and areas of geogrid are being used to stabilize the subgrade below the structure of the bike path.

Traffic Control Information

Week of July 4, 2016

No work over the 4th of July Weekend.

Expect single lane closures under flagger control. Expect 5 to 10 minute delays.



Contact Information:

Matt Bean, Project Engineer
Federal Highway Administration

Questions/Comments:

Phone: (360) 607-4061

Mailing Address:

PO Box 1155
Seward, AK 99664
