



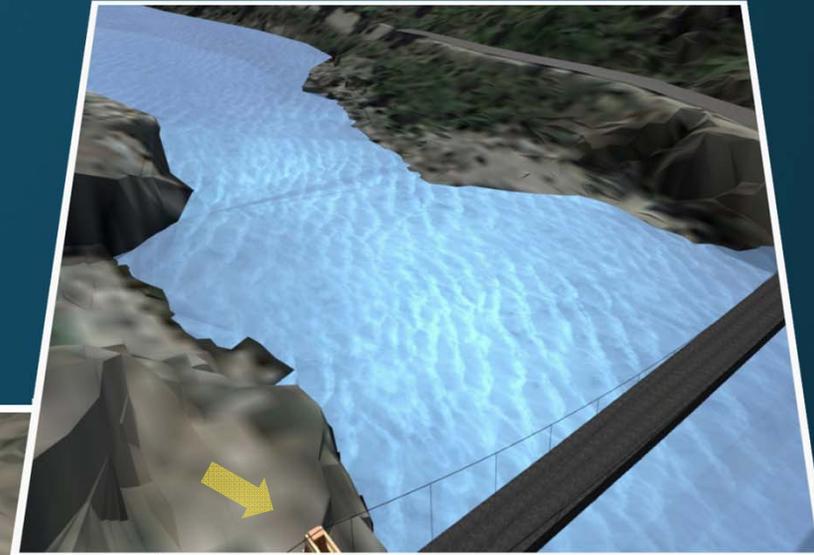



# Manning Crevice Bridge

Construction  
Sequencing

August 5, 2015  
(Relocated East Anchor)


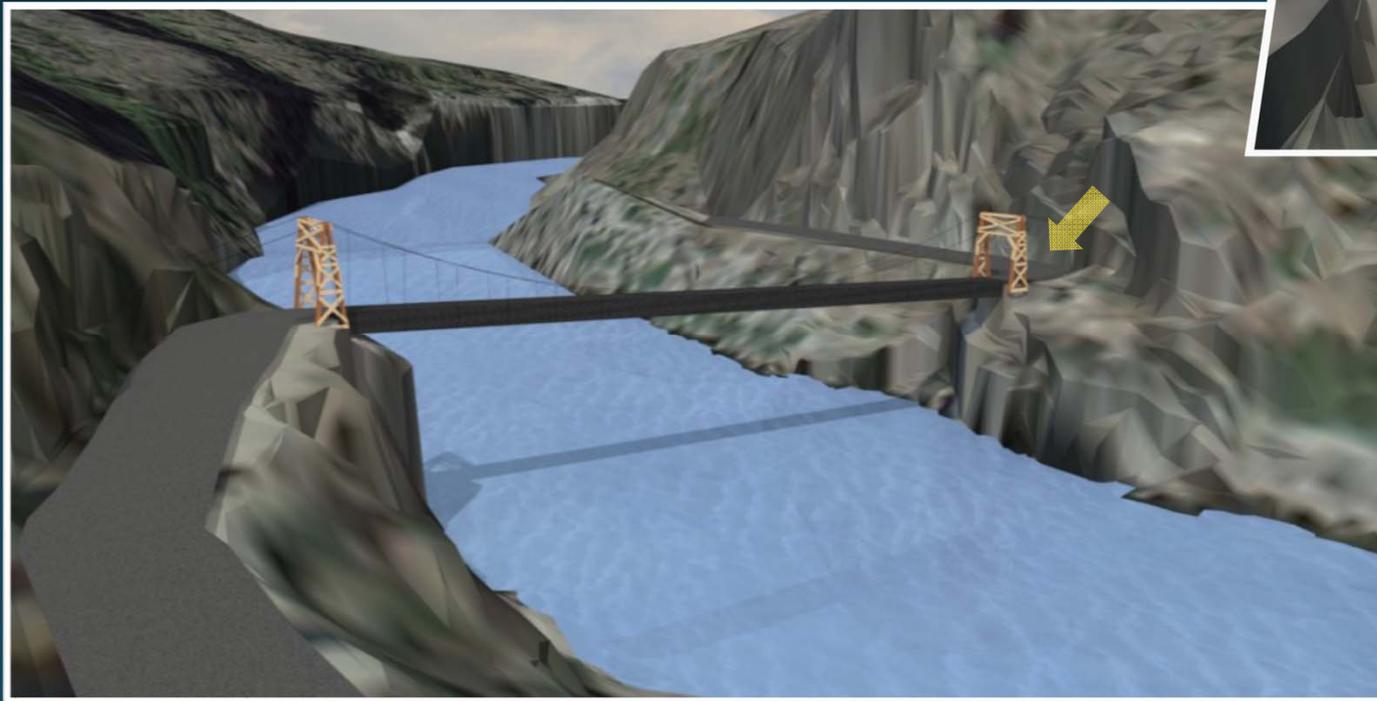


August 17, 2015  
(Install South Crane Pad)

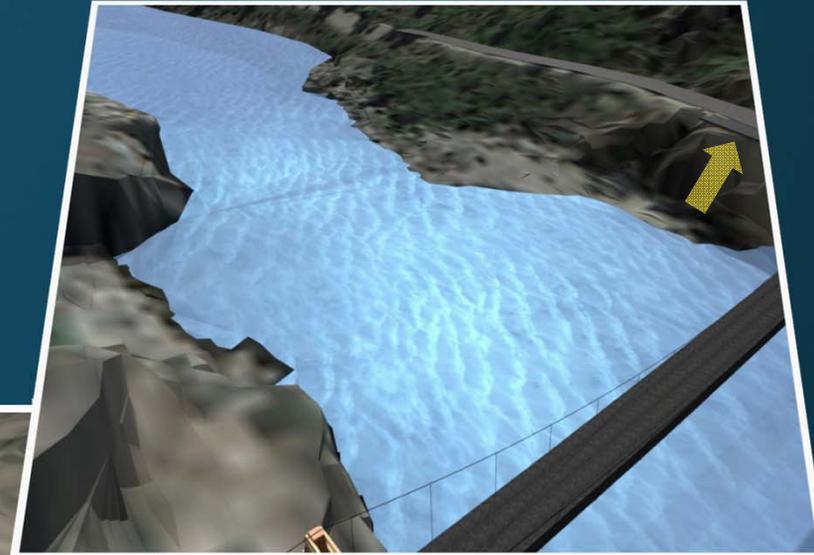
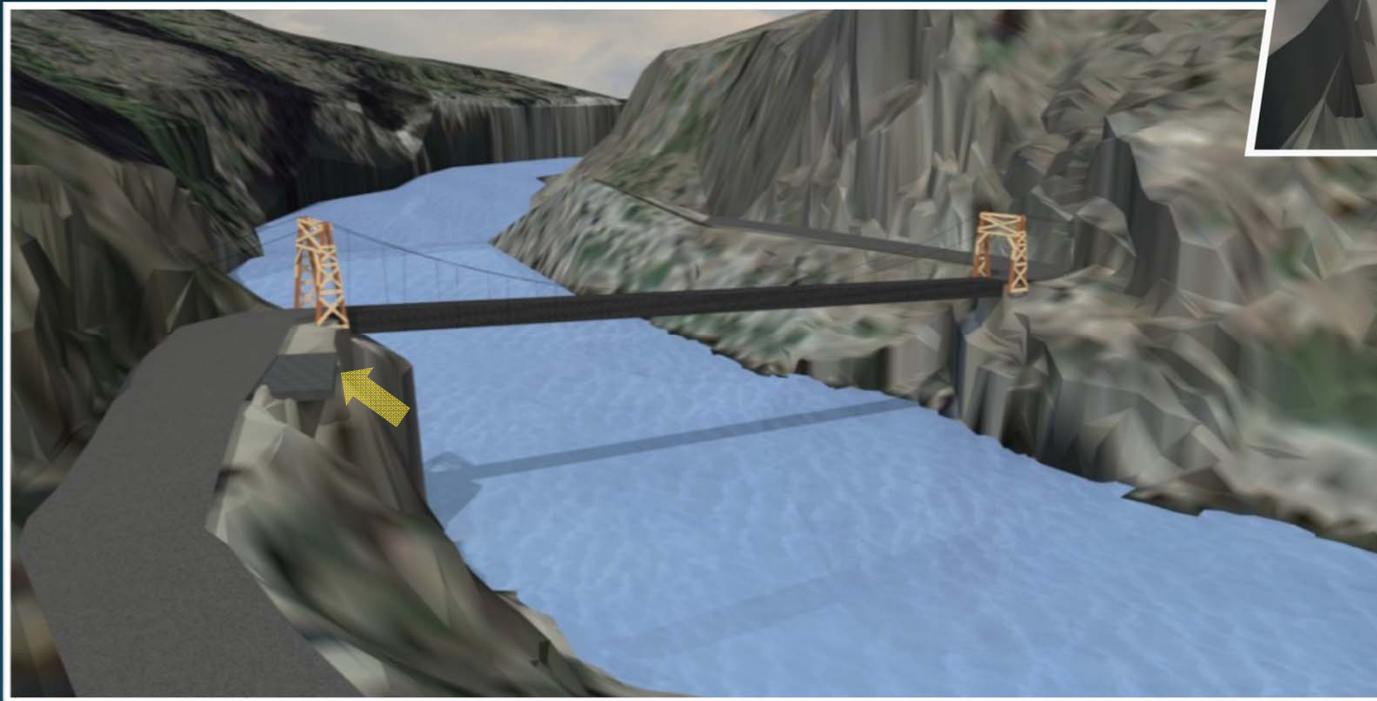


# September 25, 2015



(Install Abutment 1)

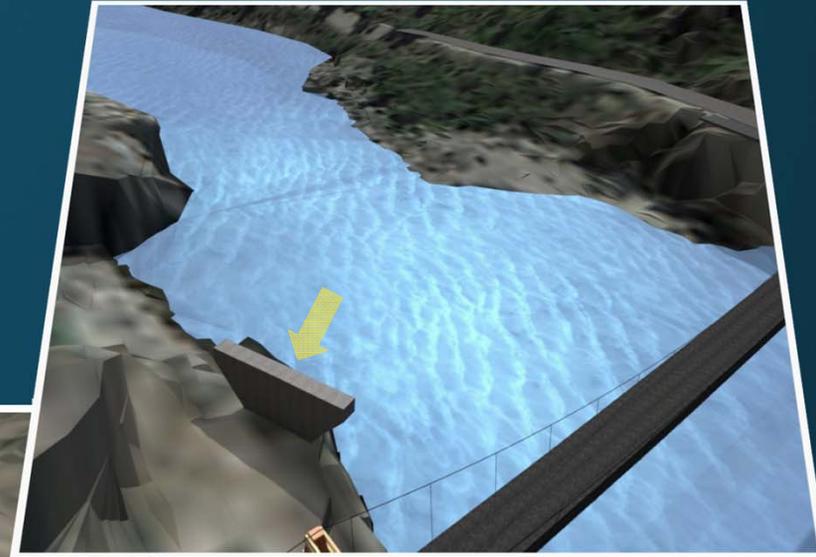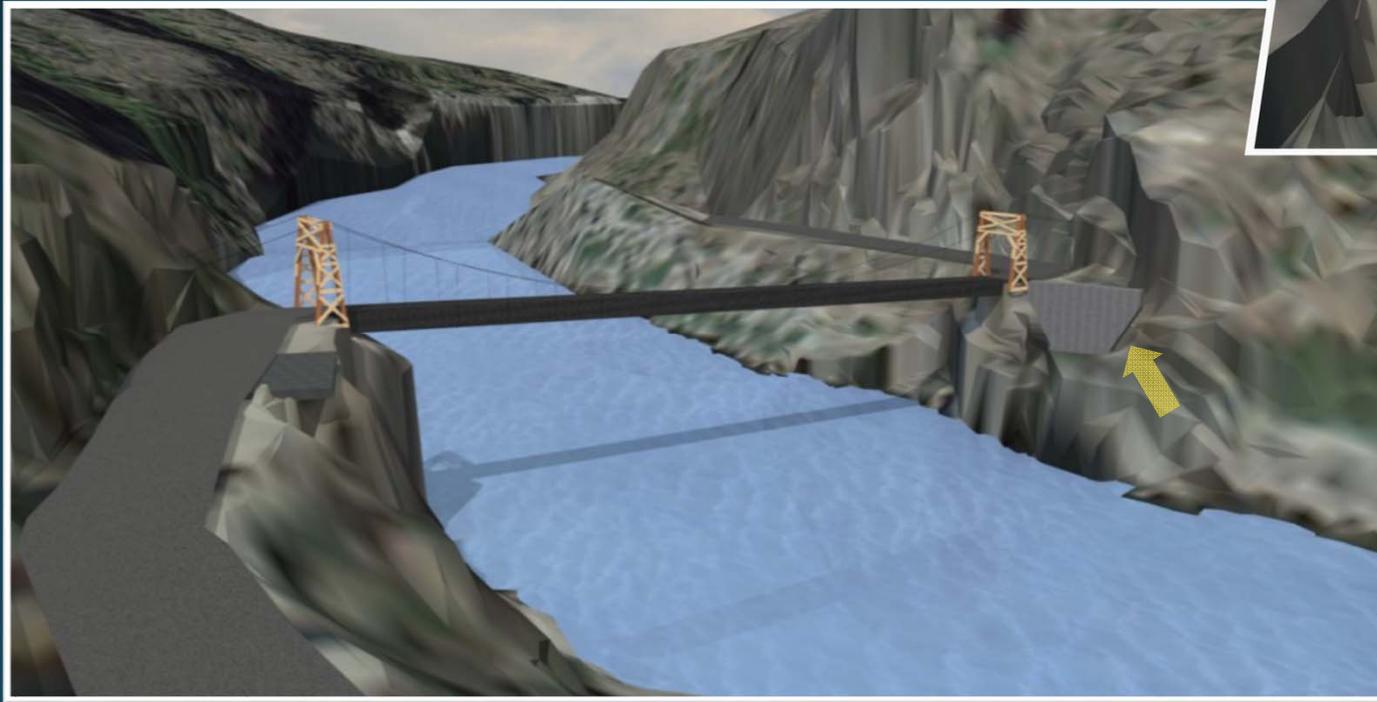



September 29, 2015  
(Wingwall C Full Height)

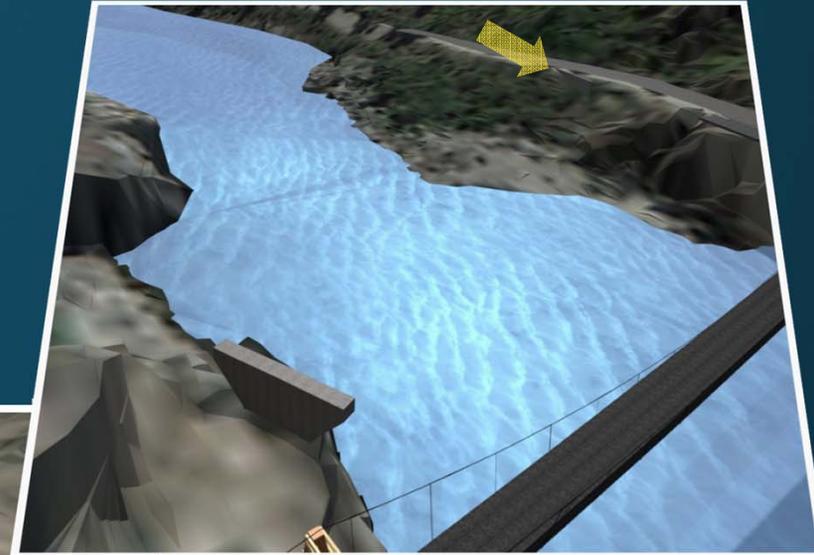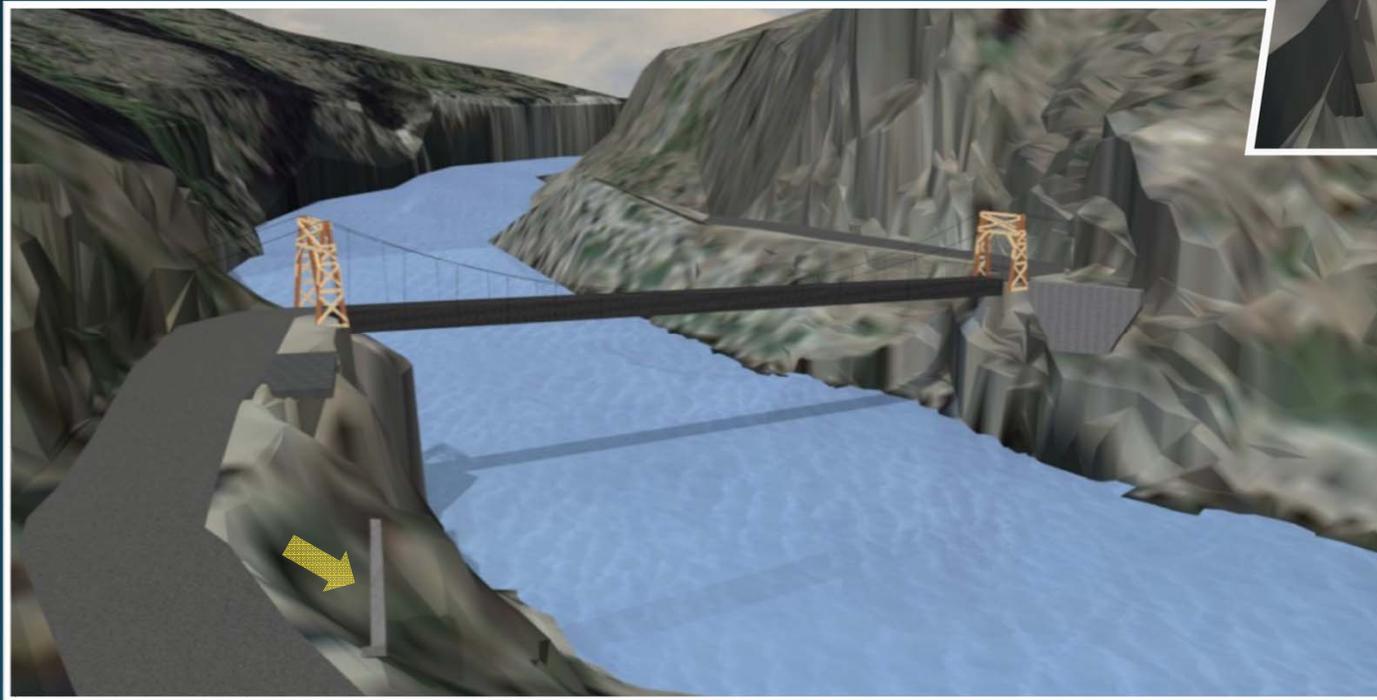

October 19, 2015  
(Wingwall B Full Height)

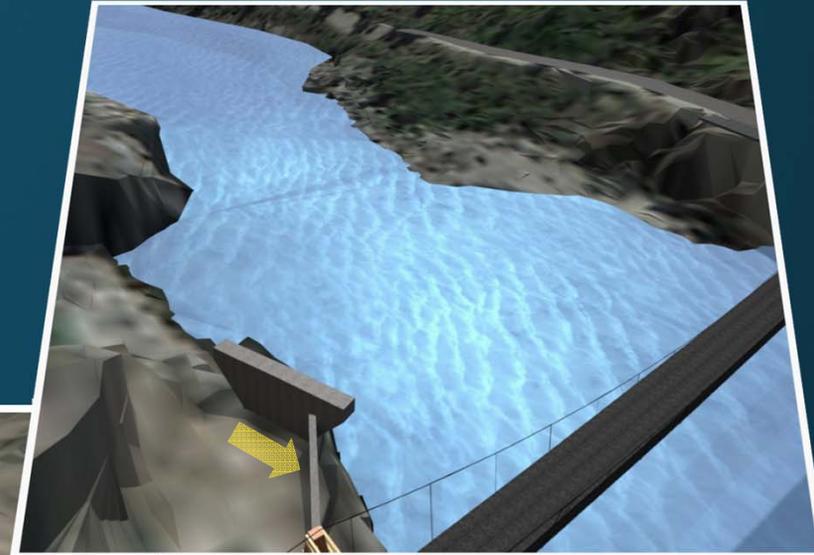
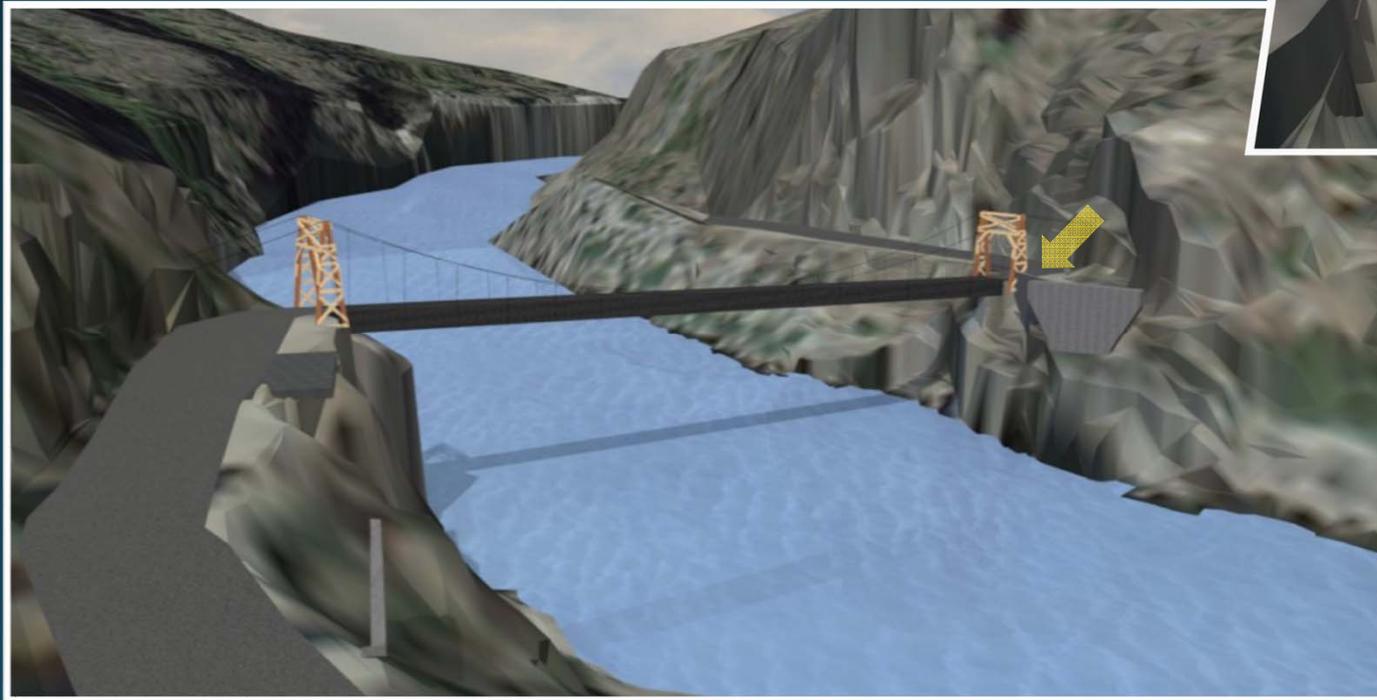


October 23, 2015  
(Abutment Saddle Piers)

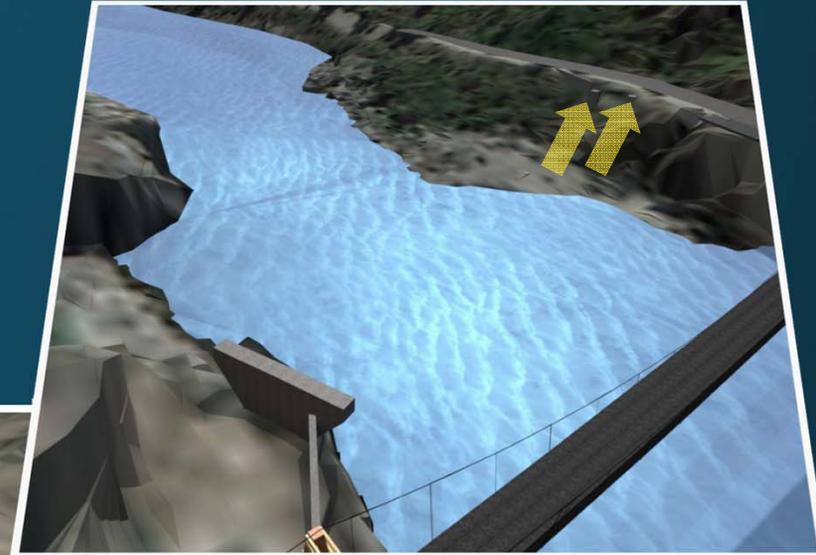
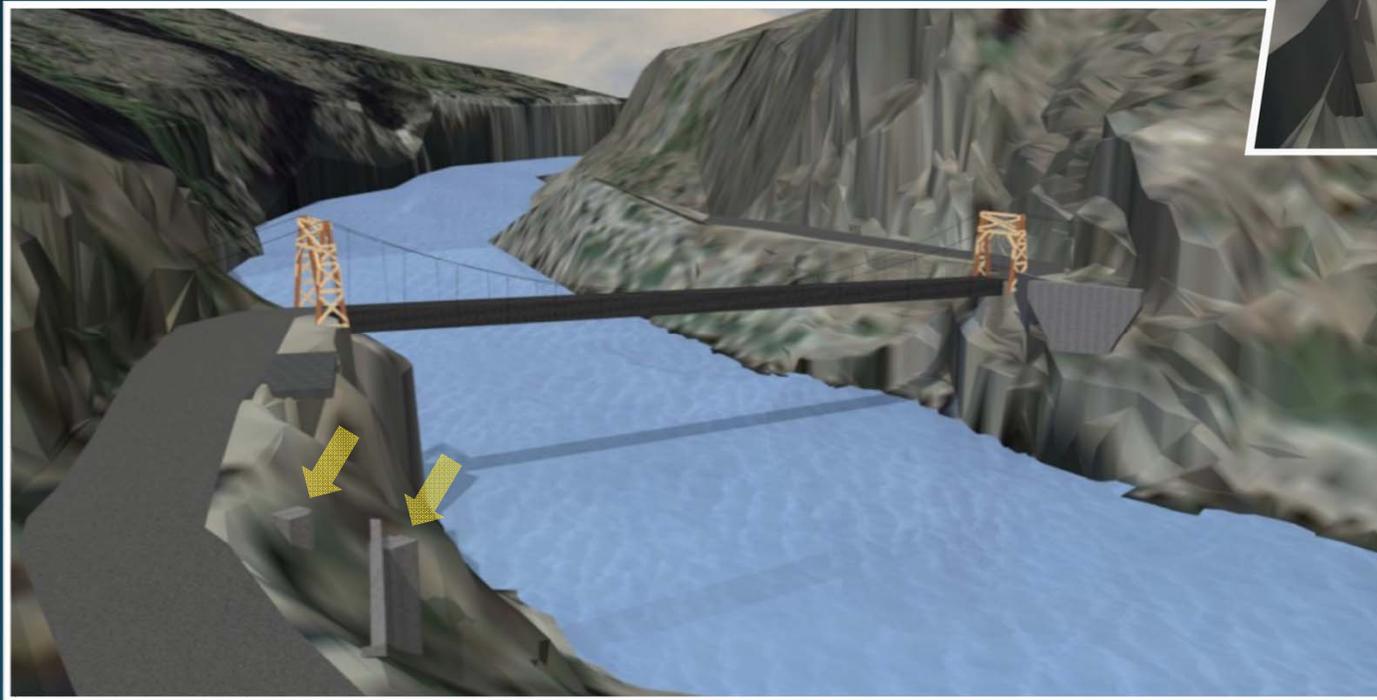


# November 4, 2015



(Girder Bearing Wall)

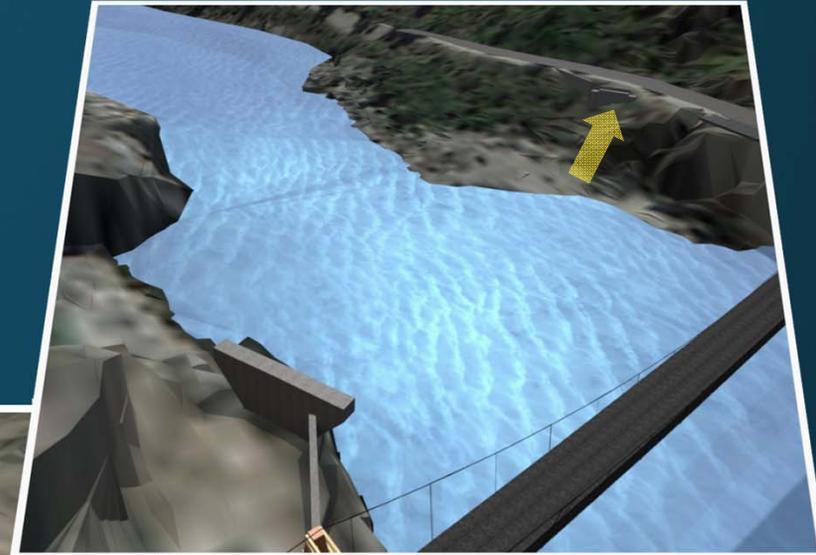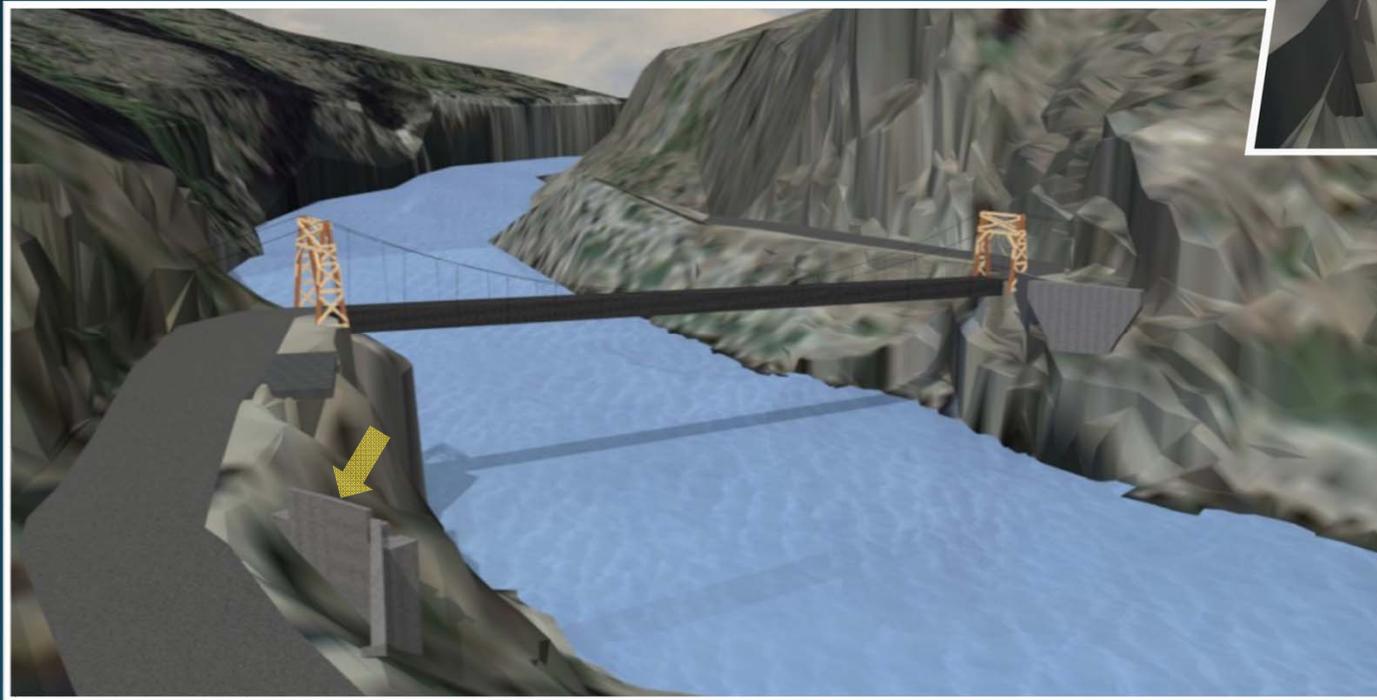

November 18, 2015  
(Pony Infill Walls & Back Cavity Wall)

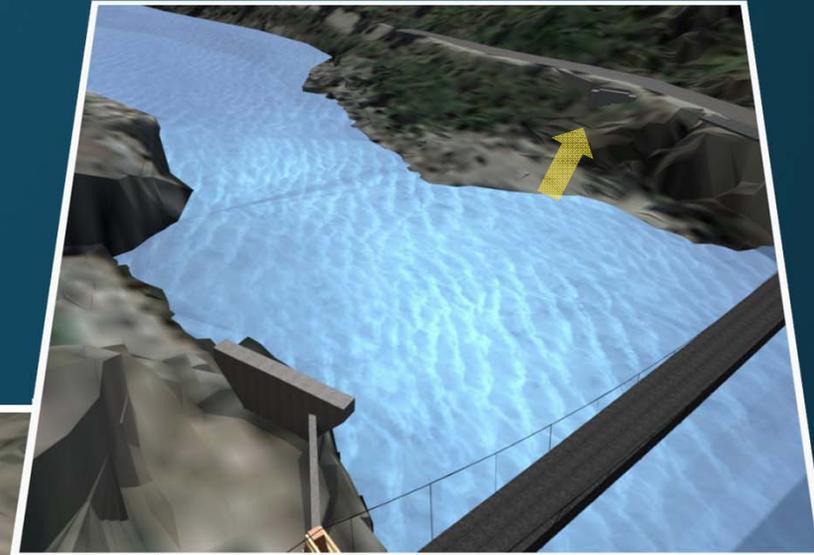
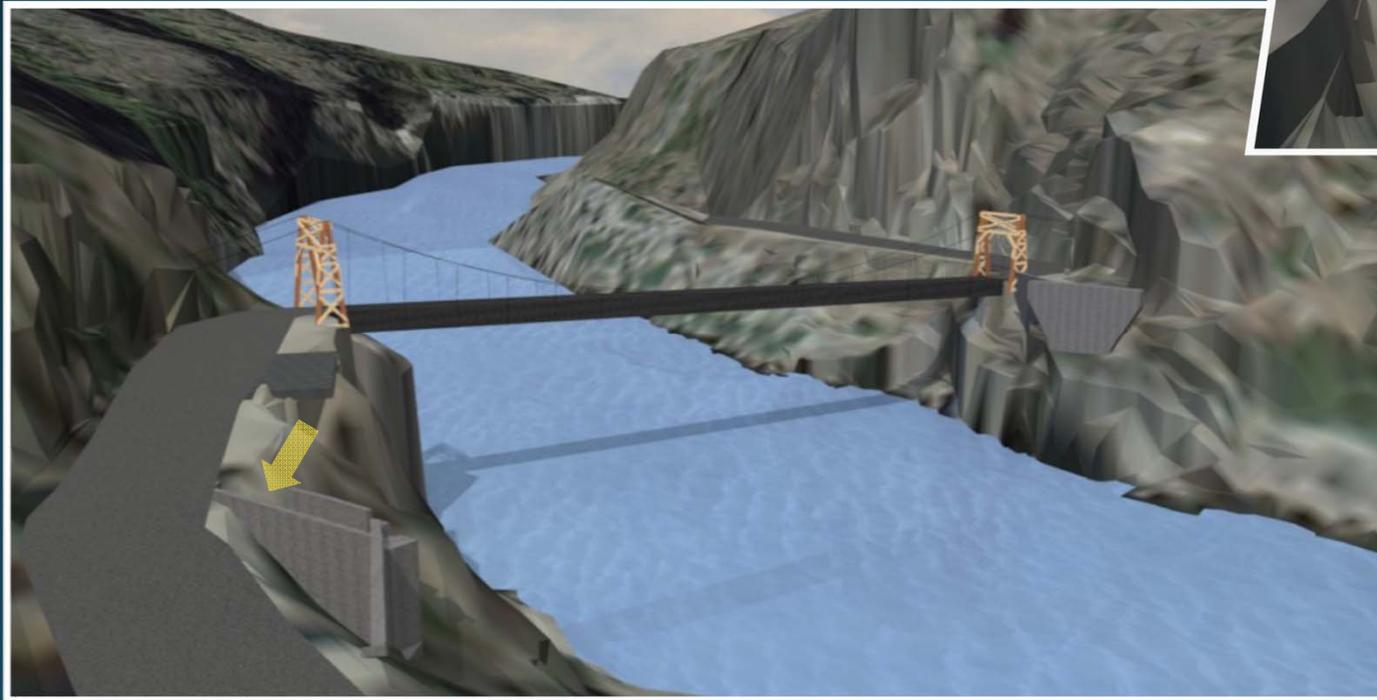


November 24, 2015  
(North Crane Platform)

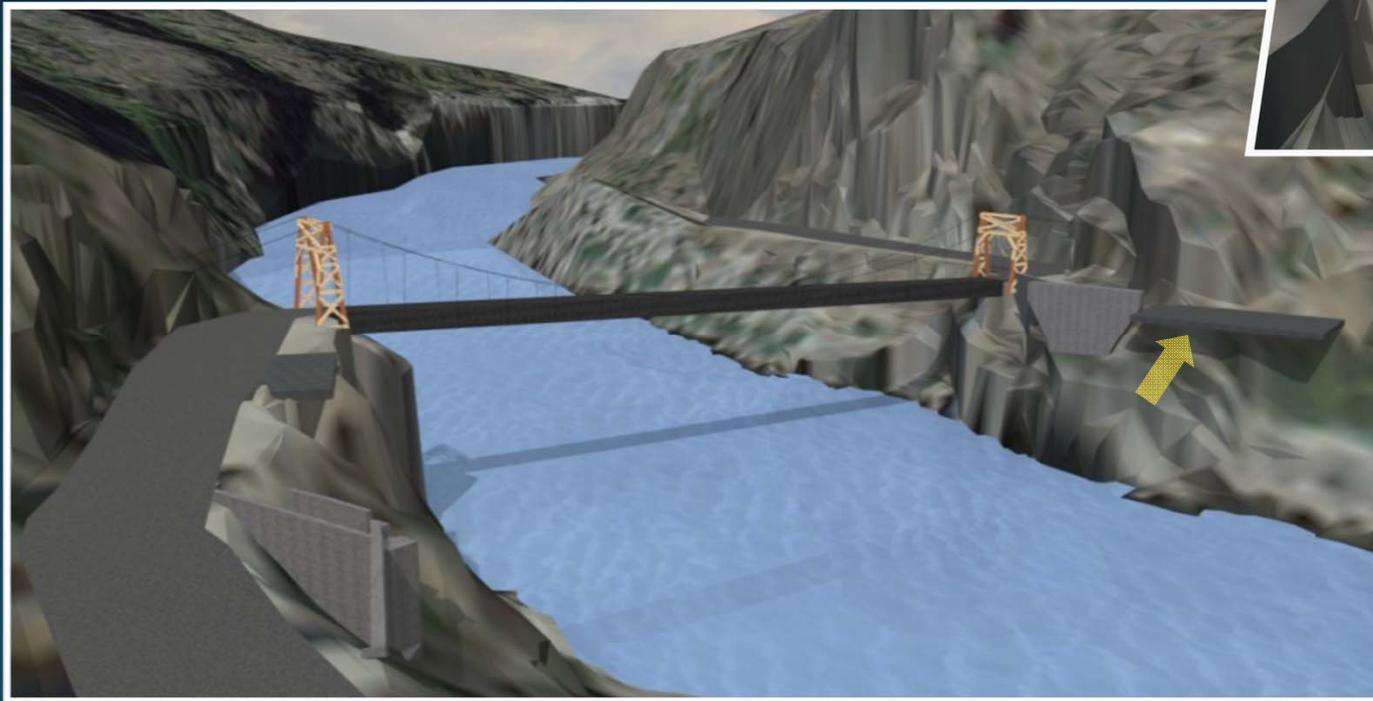
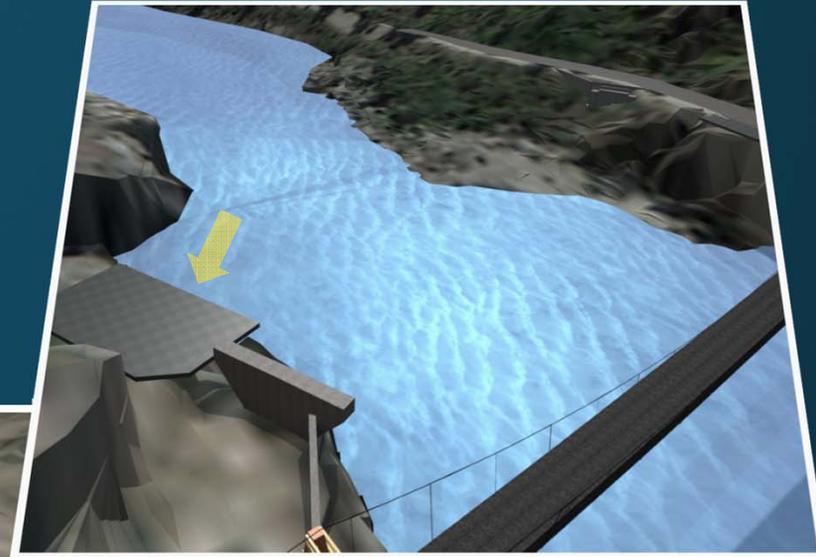


January 21, 2016

(North Anchorage Blocks)

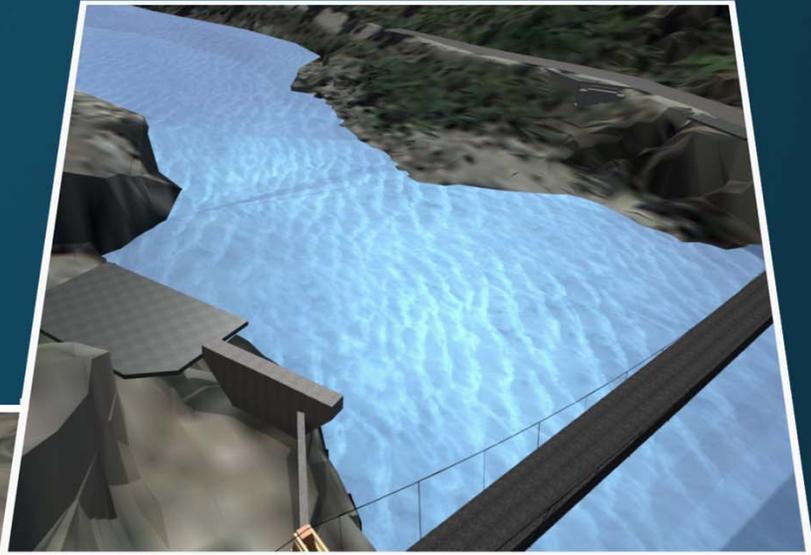
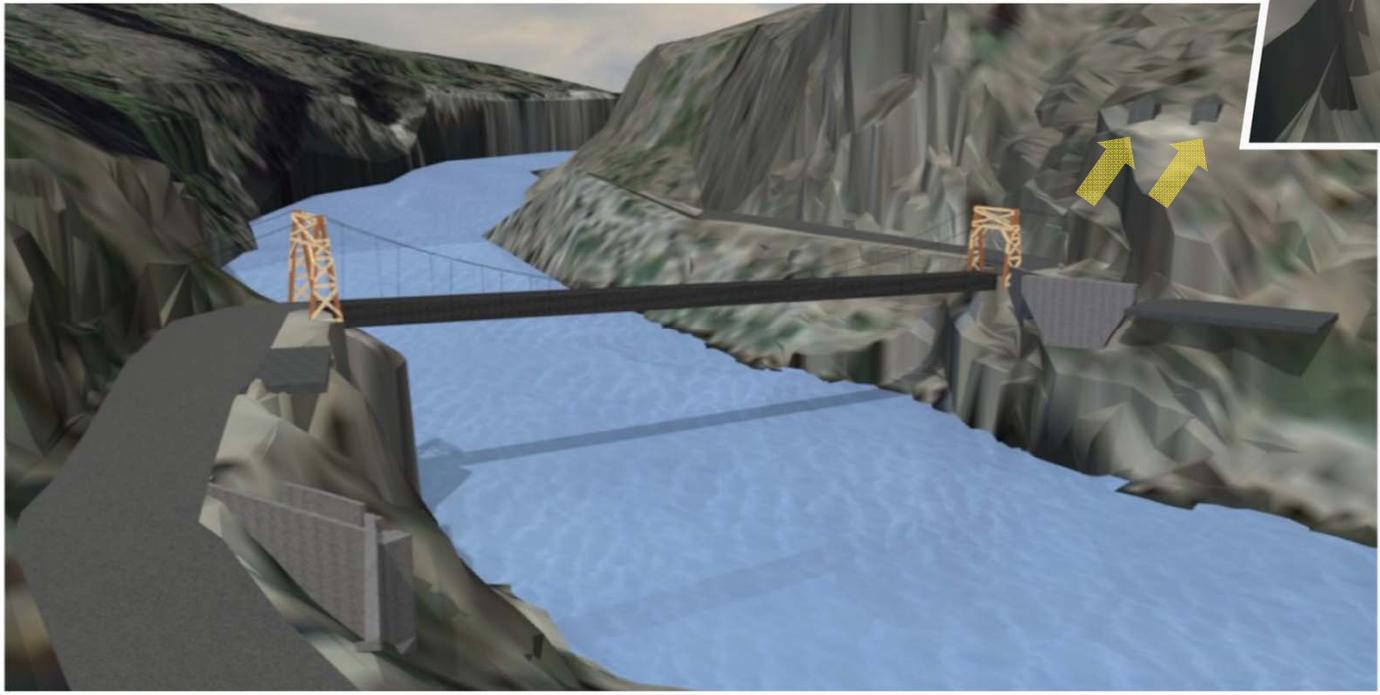


March 7, 2016  
(Lower Tower Section)

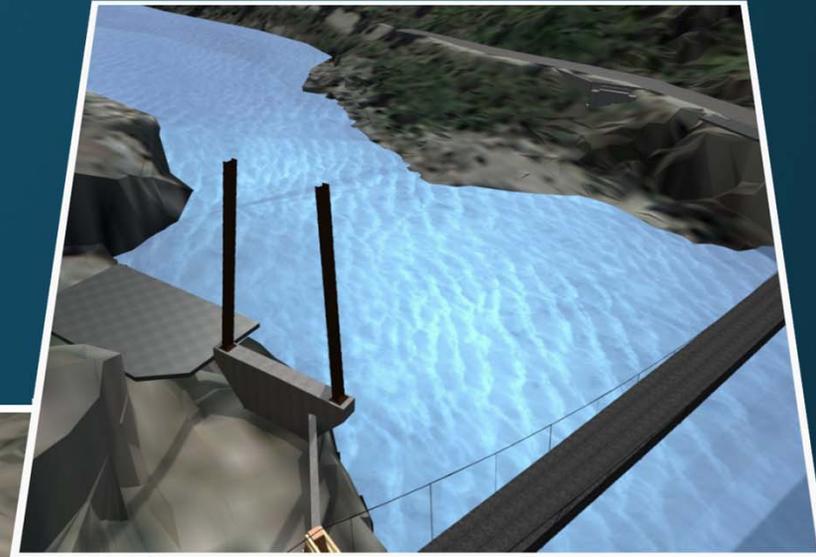
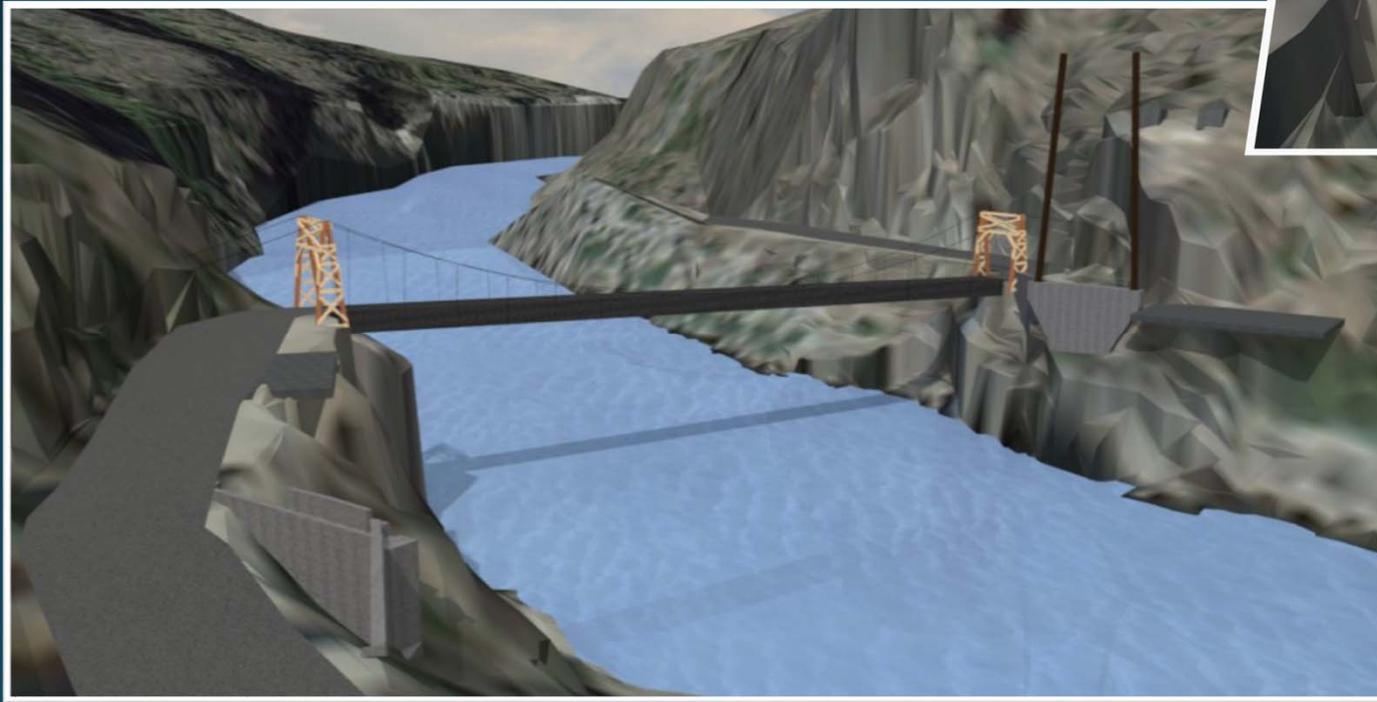


# March 14, 2016

(Mid Tower Section, South Gabion Wall & Pipe Culvert)

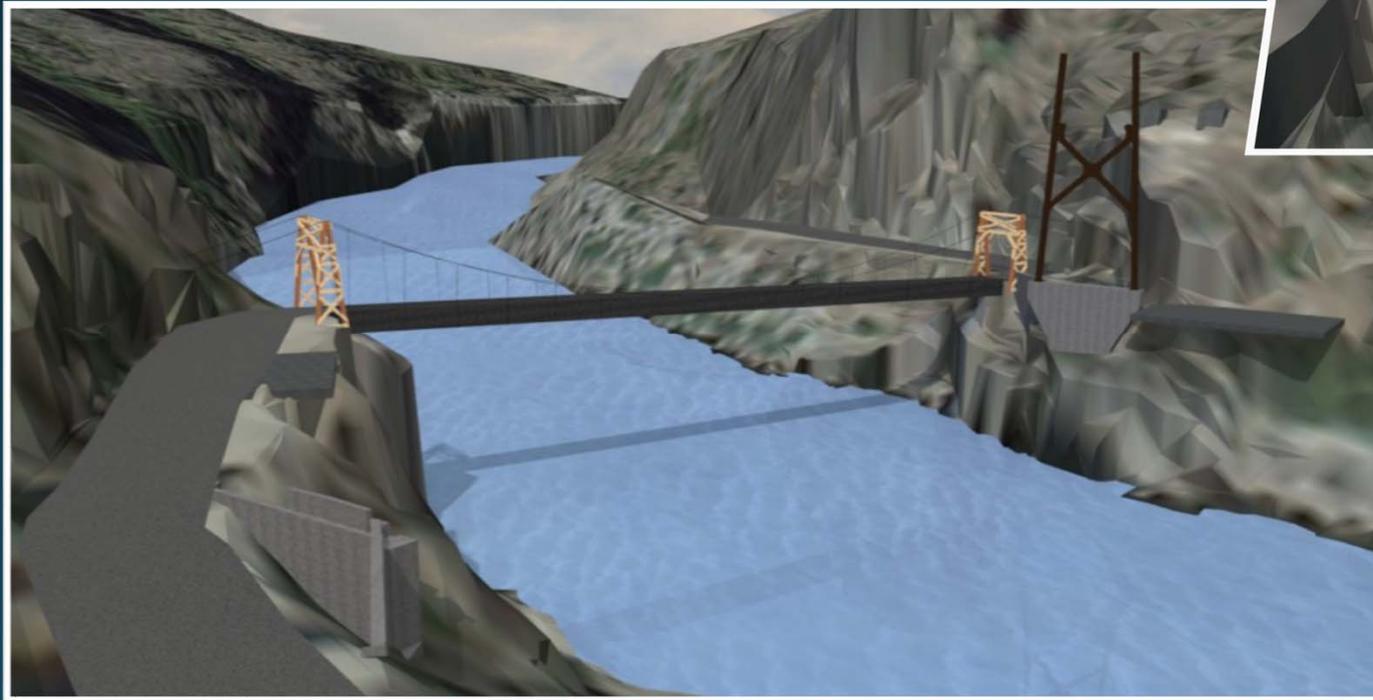
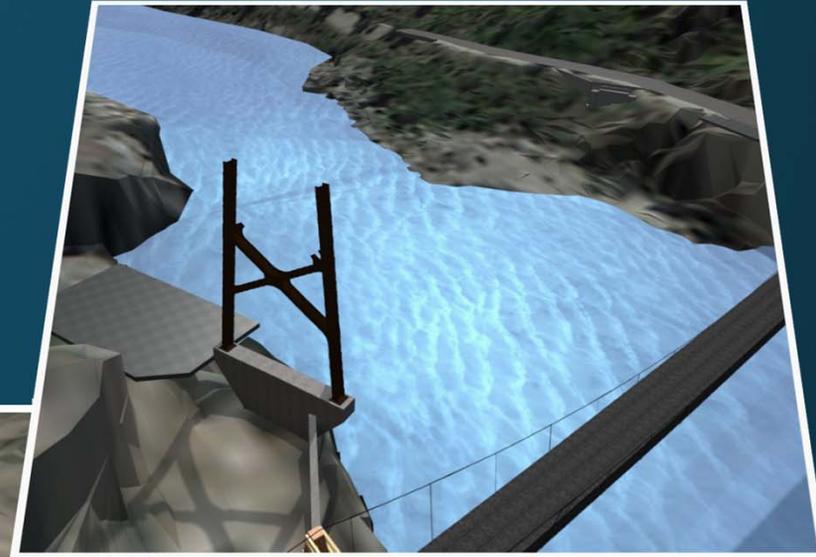


March 21, 2016  
(Upper Tower Section)

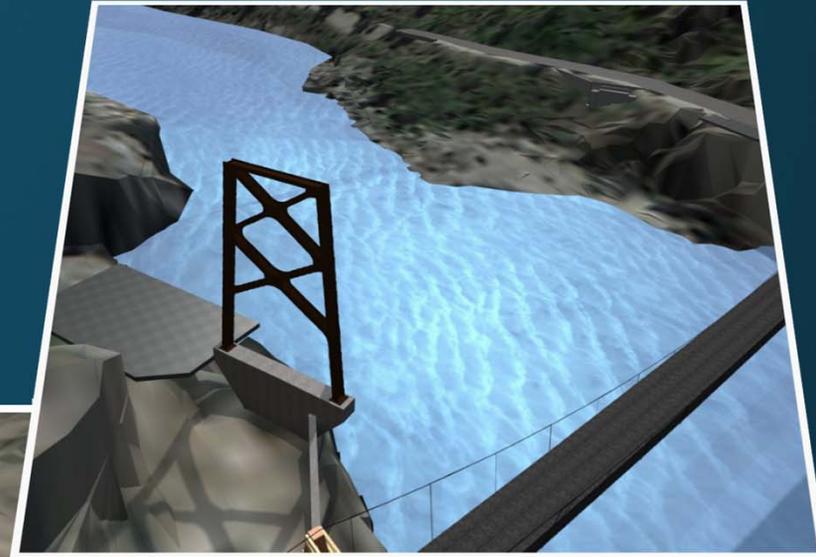
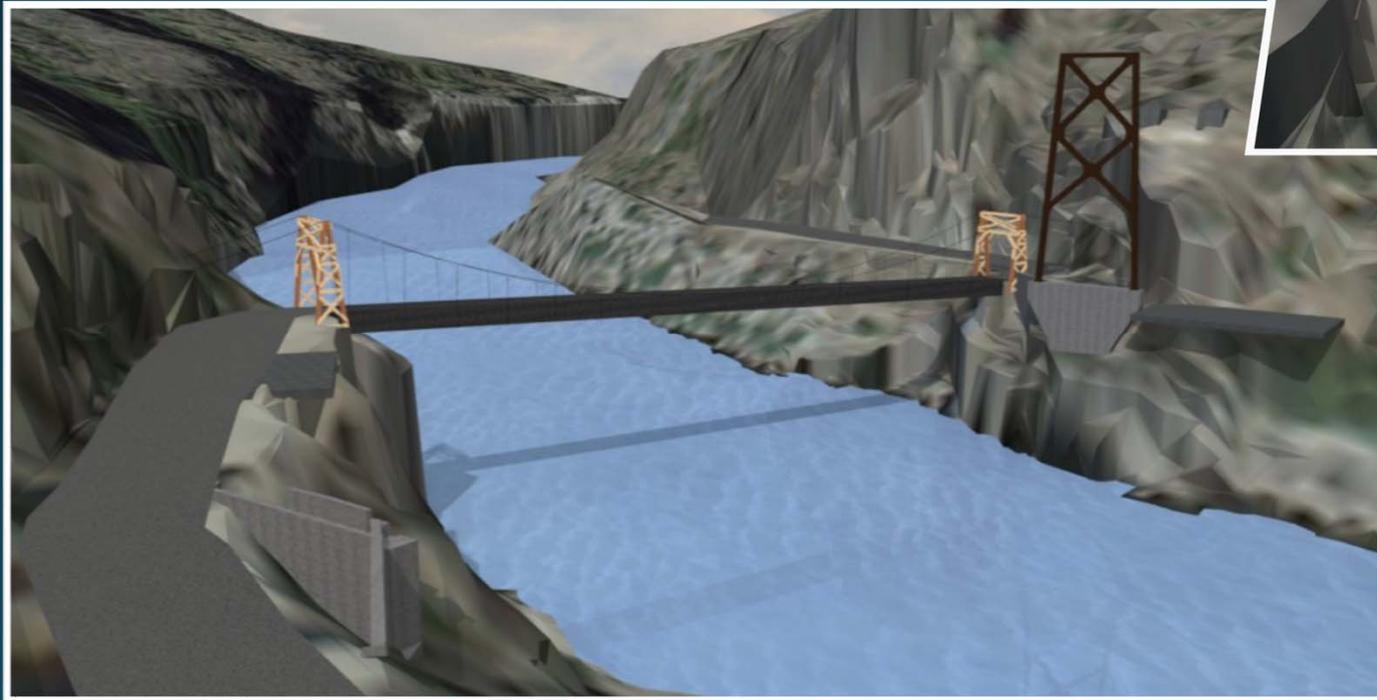


# March 23, 2016



(Cable Saddles)

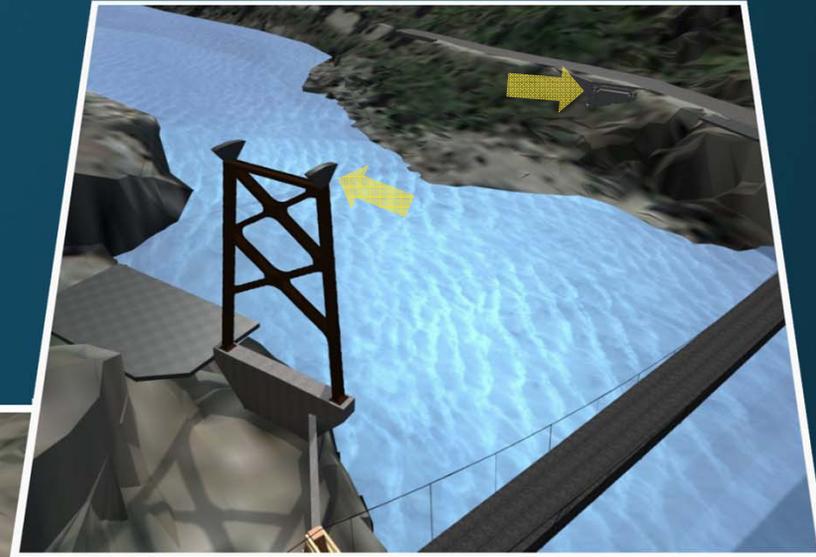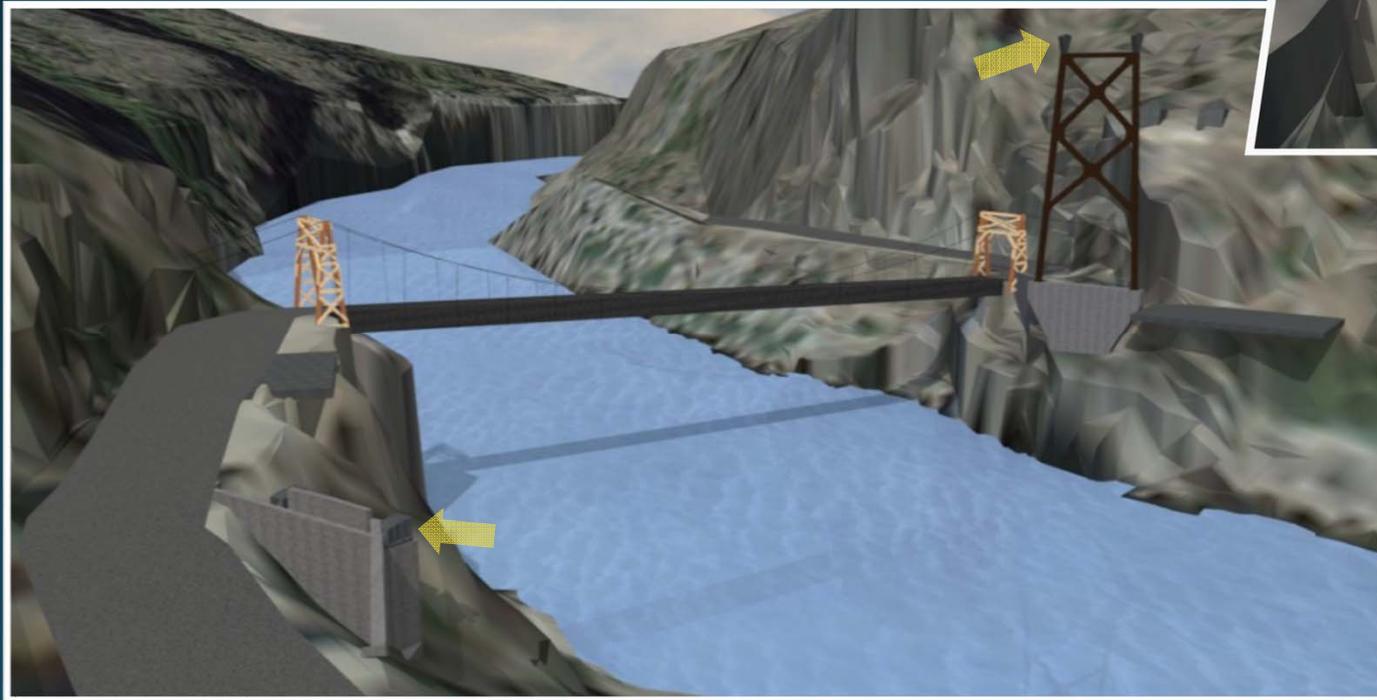



April 29, 2016  
(East Suspension Cables)

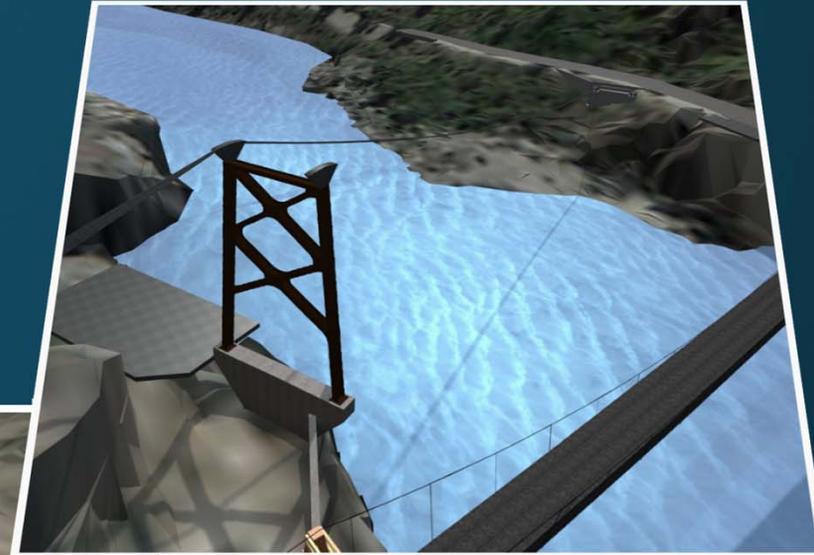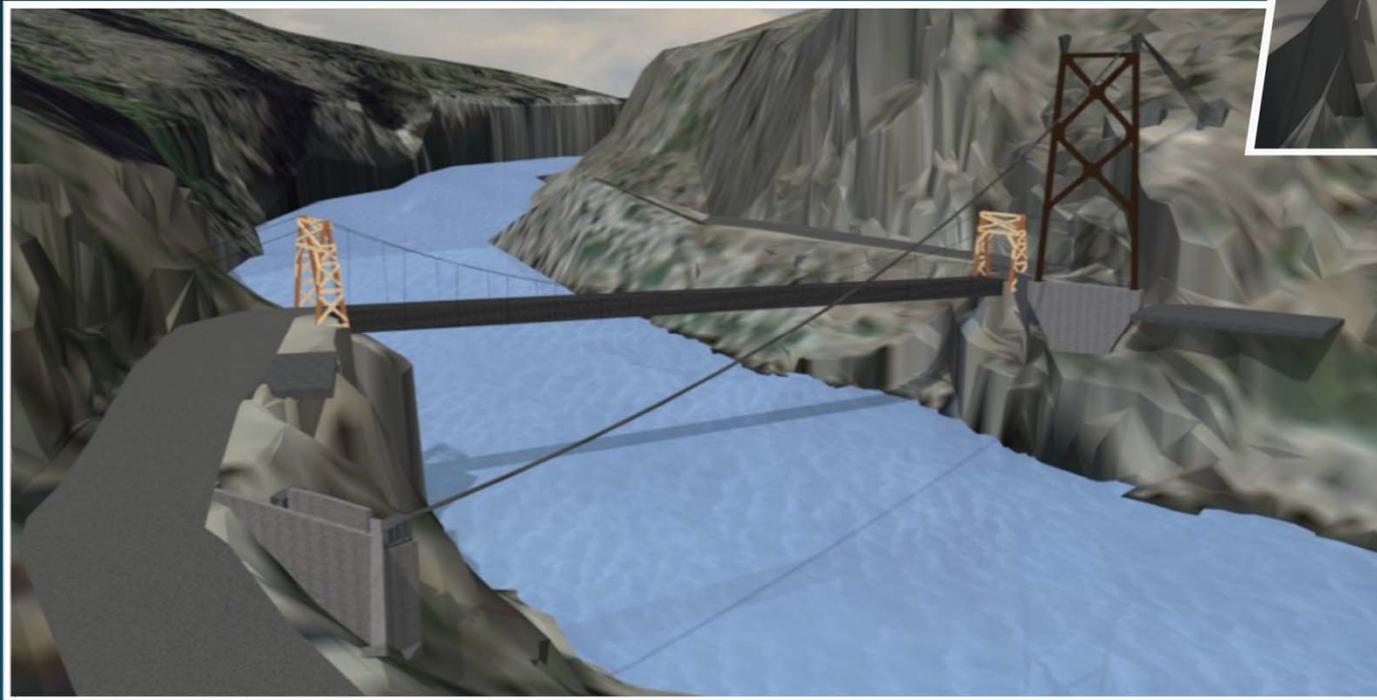



May 17, 2016  
(West Suspension Cables)

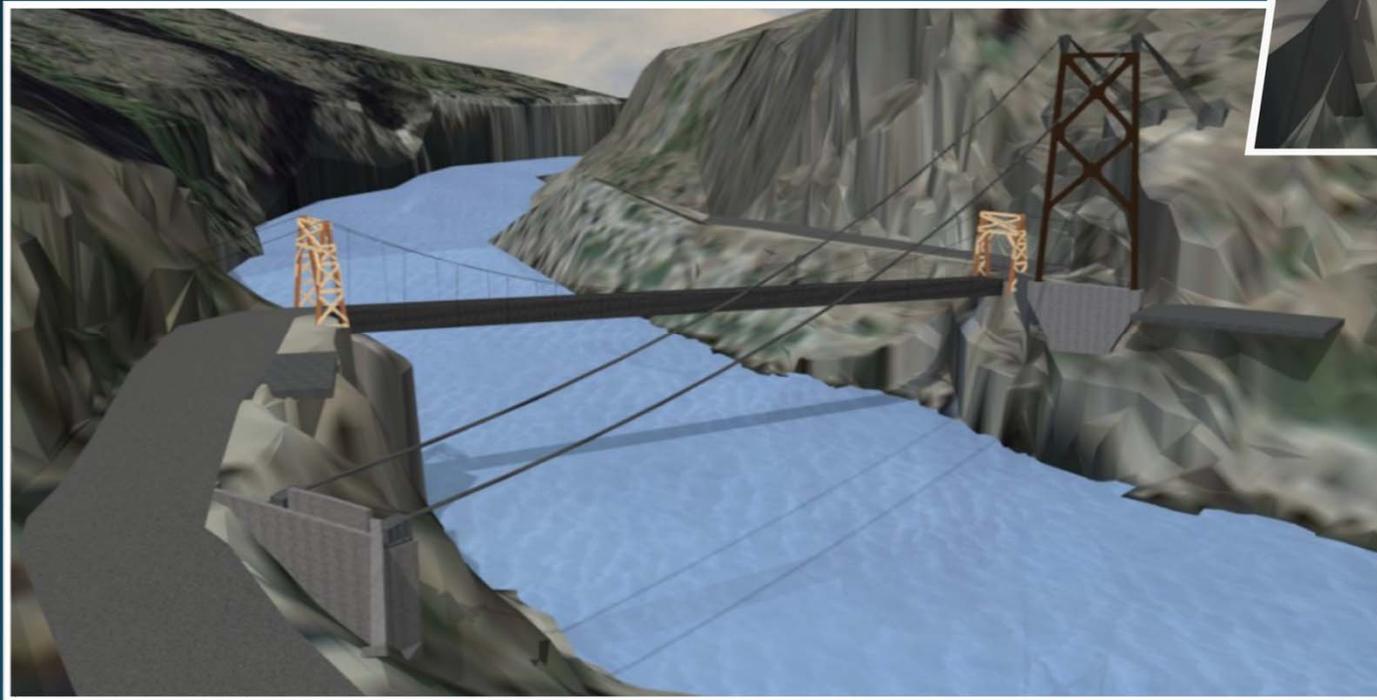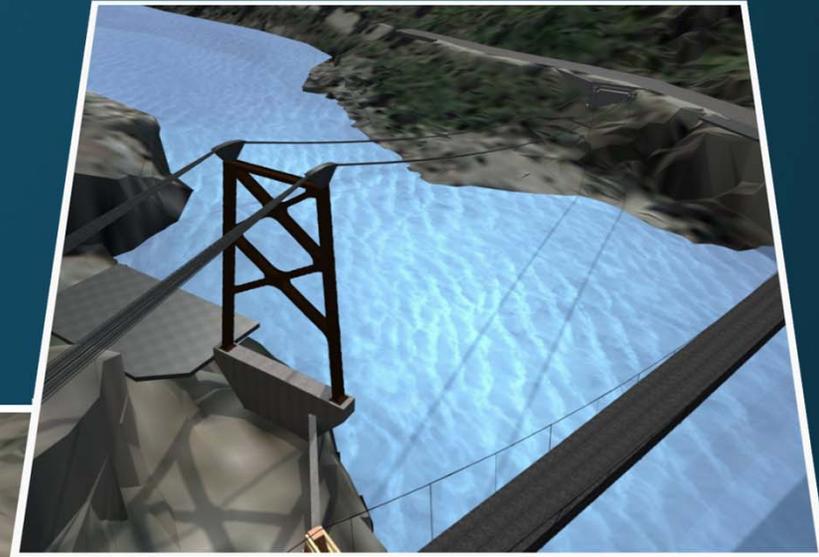



May 31, 2016  
(East Hangar Cables)

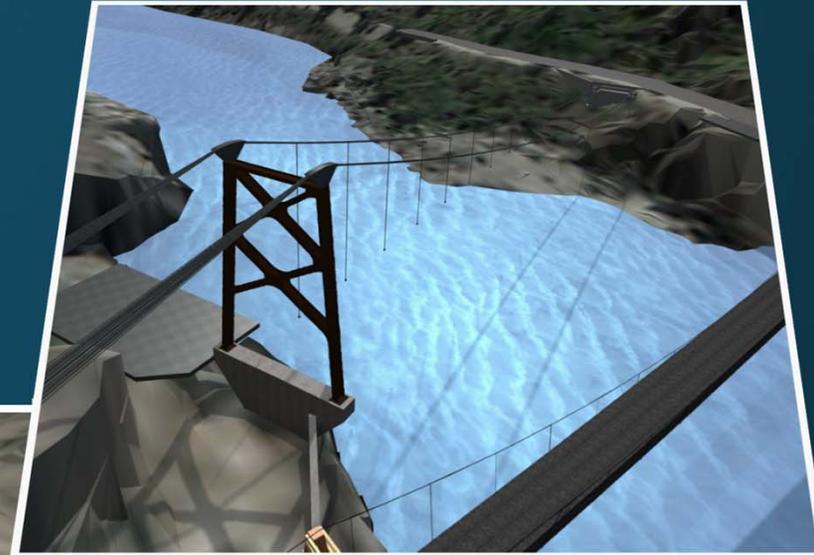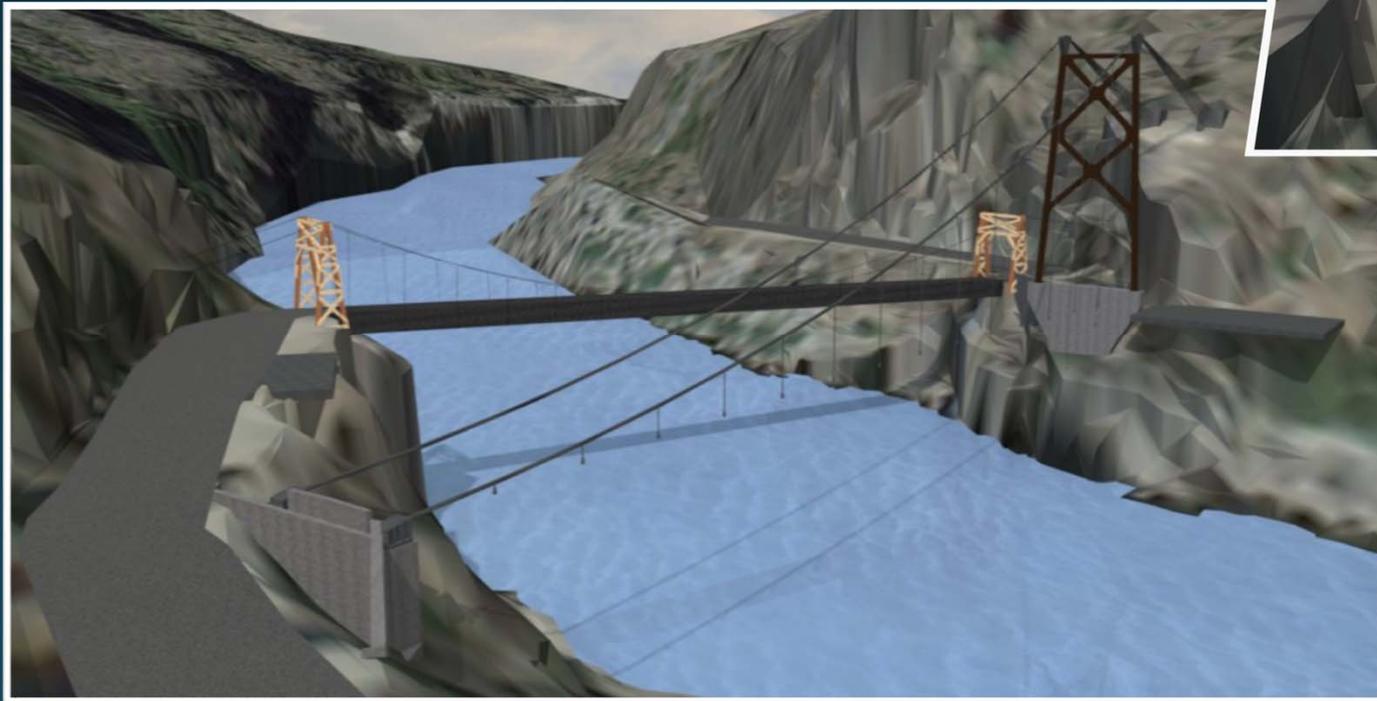

June 7, 2016  
(West Cable Hangars)

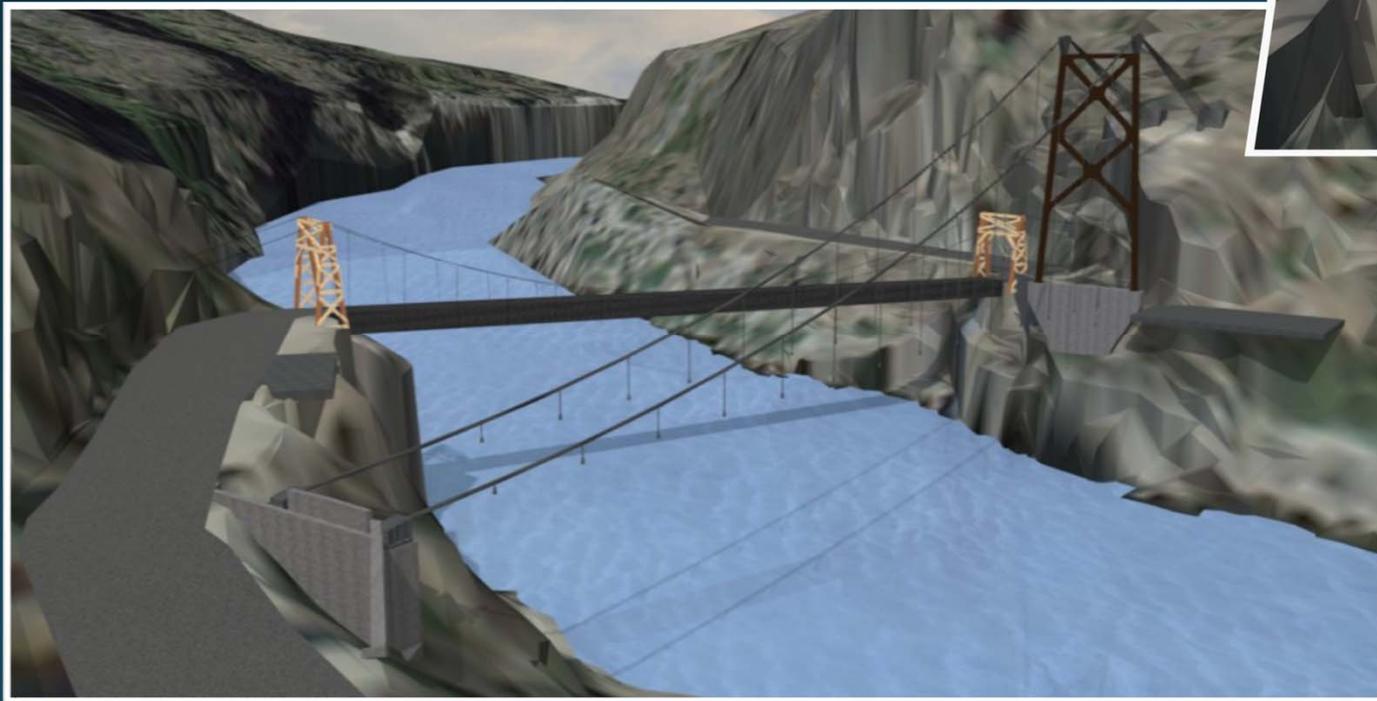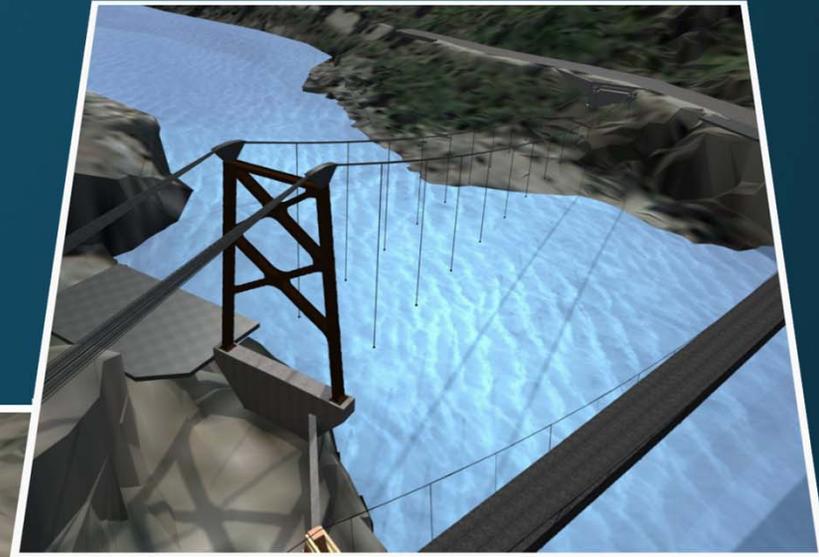


June 16, 2016  
(Floor Beams)

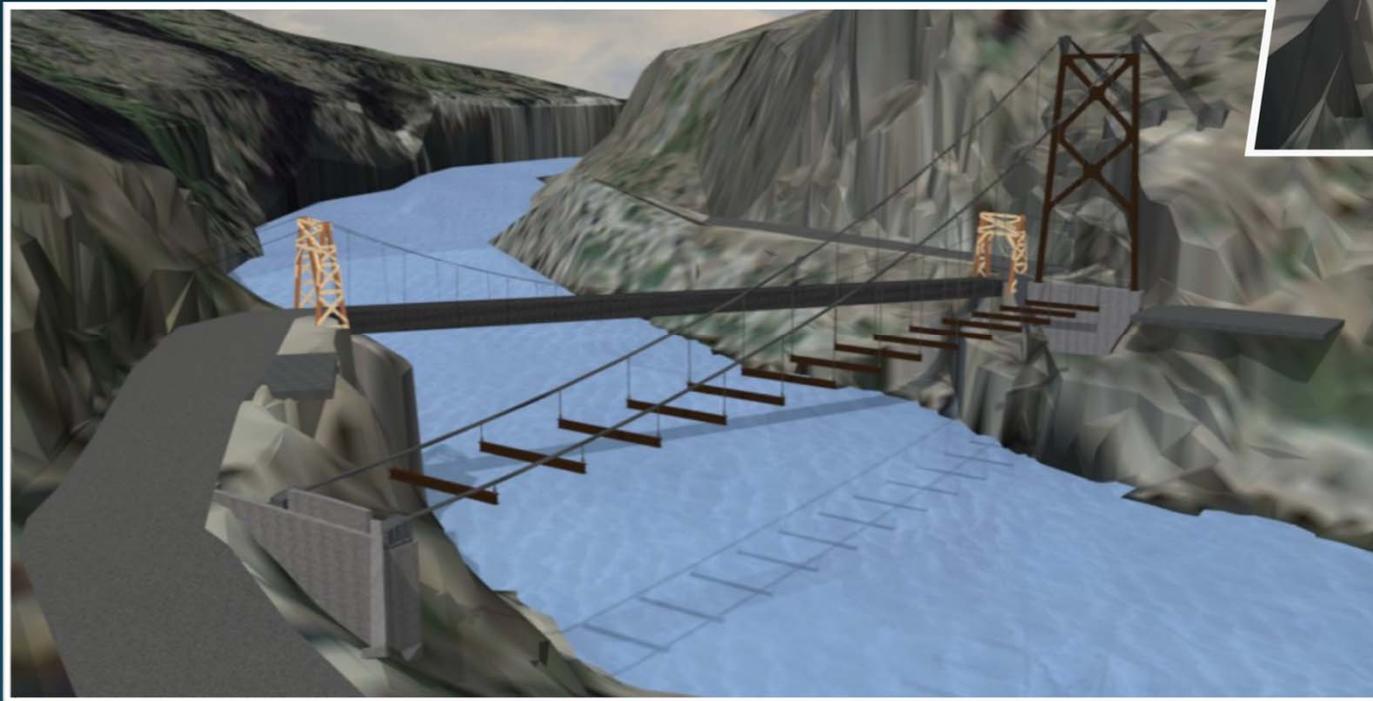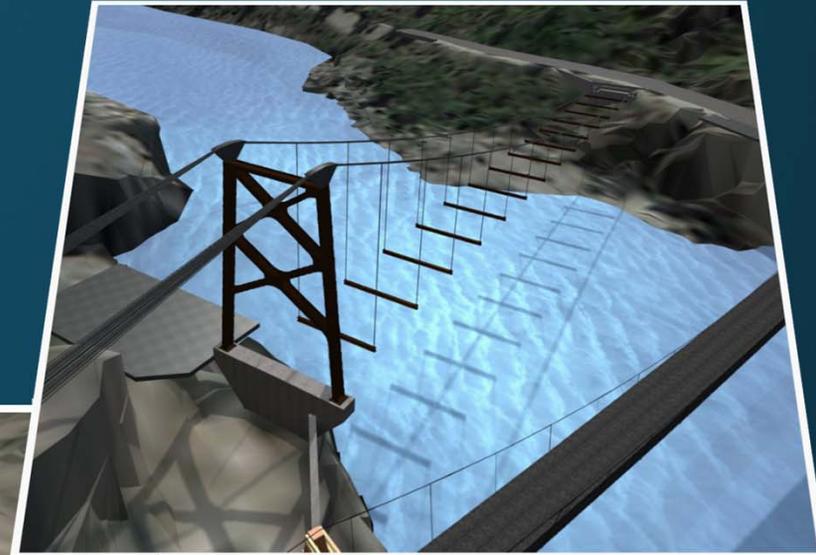


# July 7, 2016



(Stiffening Girders & Diaphragms)

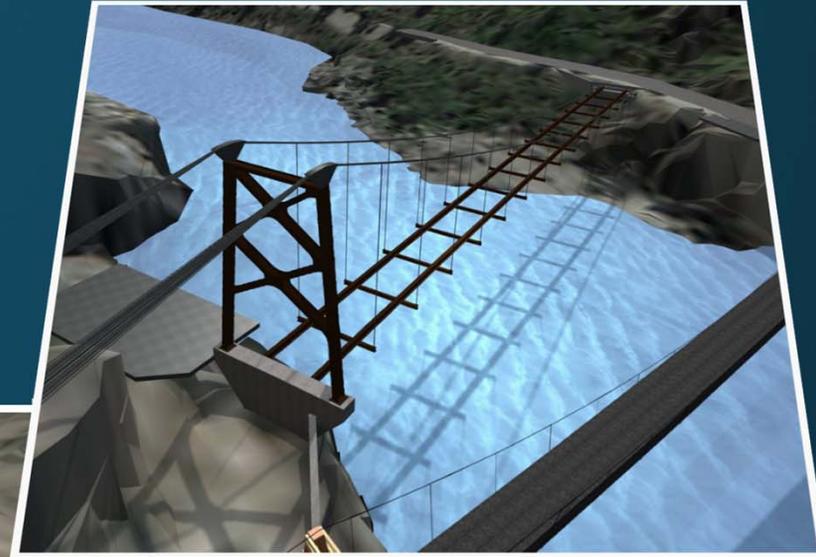


July 28, 2016  
(Abutment Elevated Slab)

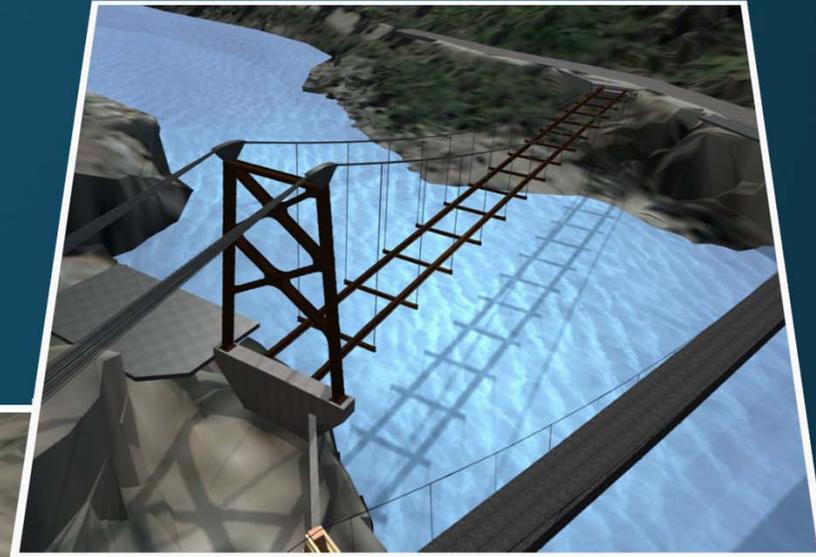


August 23, 2016  
(South Deck)

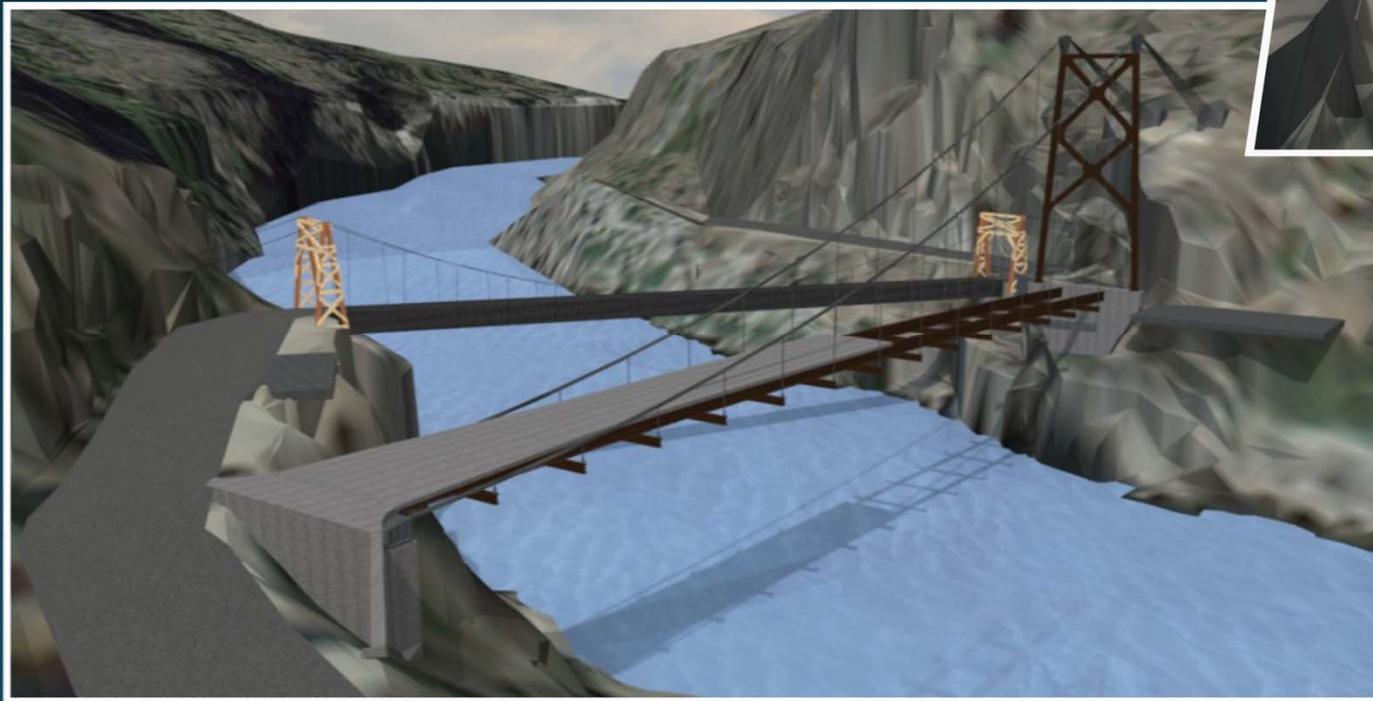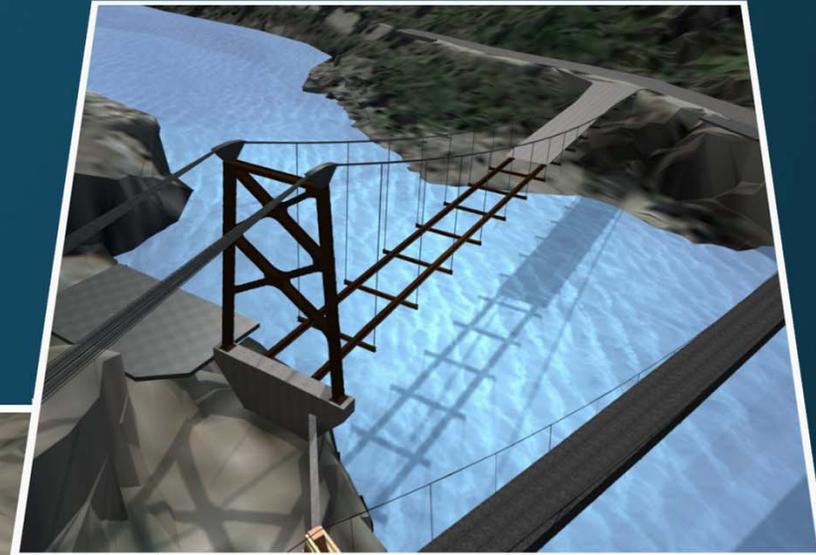

August 31, 2016  
(North Deck)

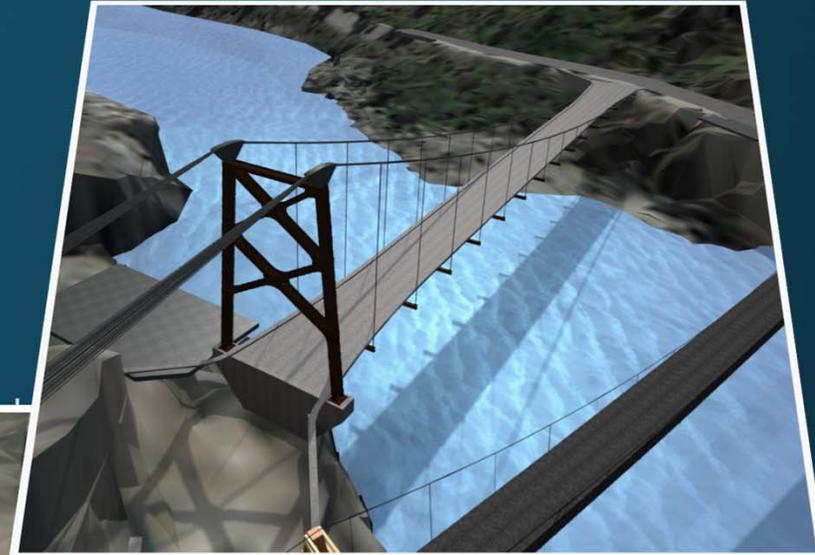

September 22, 2016  
(Curb)

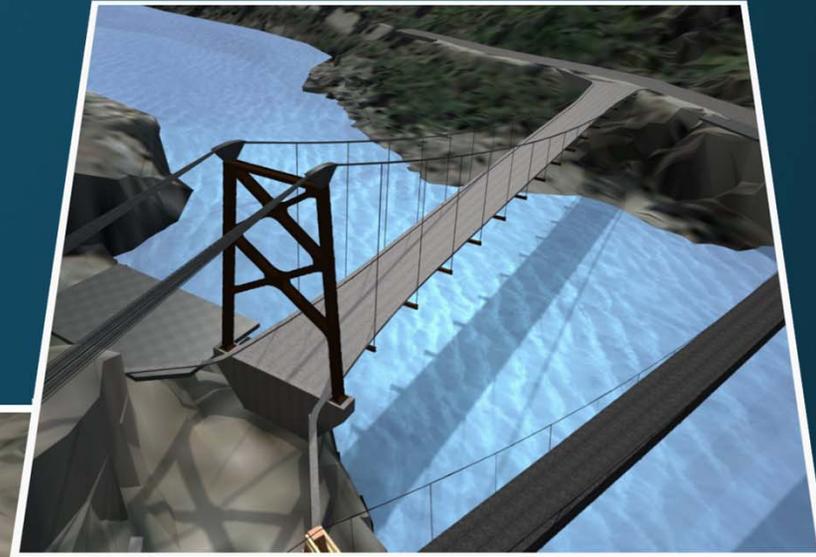


October 7, 2016  
(Two-Tube Rail)




# October 19, 2016

(Remove North Crane Pad)

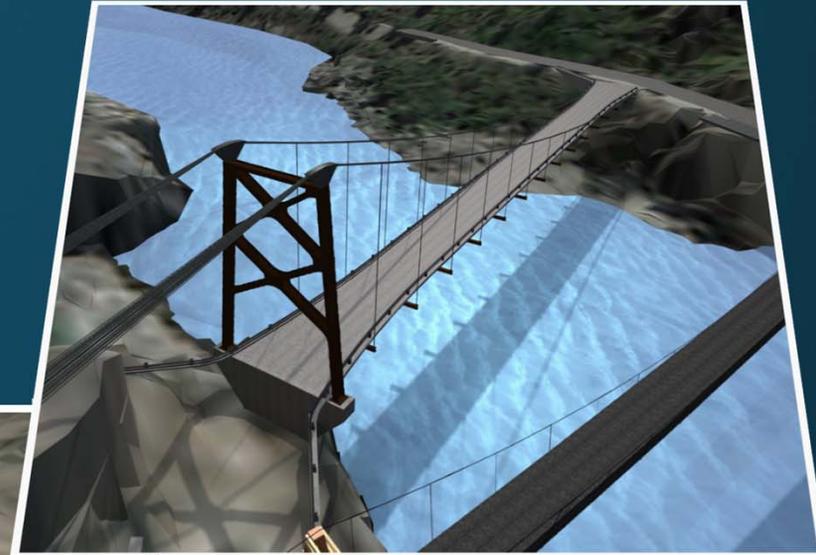

October 31, 2016  
(Wingwall A & North Gabion Wall)

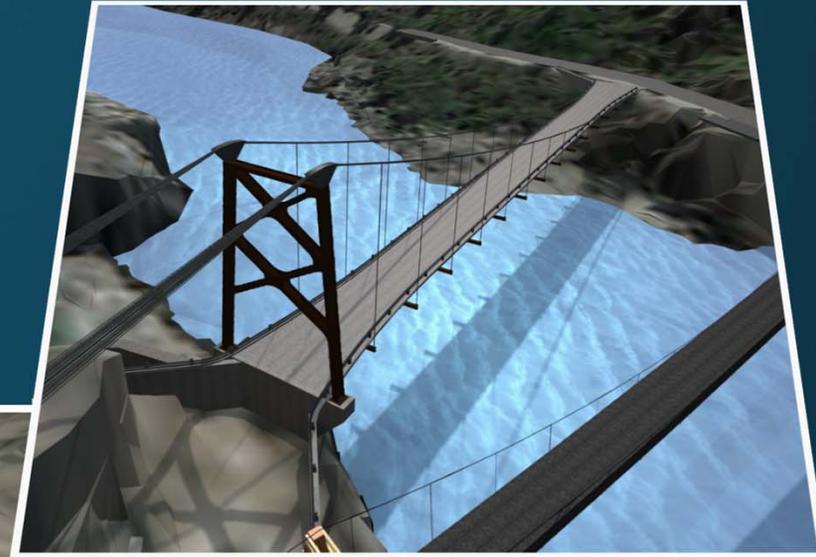

# November 4, 2016

(North Approach Slab & Bridge Demolition)



# November 24, 2016

(Asphalt Paving)



# Finished Bridge

