

Cattle Point Road Relocation

CONSTRUCTION NEWSLETTER

June 12, 2015

Excavation and Embankment Continue

CONSTRUCTION ACTIVITIES

This week, Strider began removing topsoil and excavating along the left shoulder across from the NPS Vista. In addition to continued excavation and embankment, they shaped some completed slopes.


Next week, Strider Construction will continue with the excavation and embankment process.

Please Note: The large topsoil stockpile located left of the new alignment will need to be moved in the coming weeks. The best place for it to go is in the left lane of the existing road. Unfortunately, this means we will be down to a one lane road for about 500 feet. Traffic will be controlled using traffic signals.

Removing Topsoil



Shaping the Slope

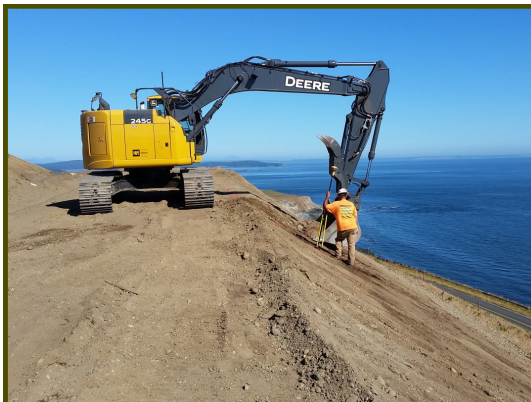

Shaping the Slope as seen from the Road.



WORK SCHEDULE

Monday 8:30 - 6:00

Tue - Thu 7:00 - 6:00

Friday 7:00 - 3:00

DELAYS AND CLOSURES

NPS and DNR Vistas are Closed.

Delays: up to 15 min from 6 am to 8 am / up to 30 min from 8 am to 6 pm

Mt Finlayson eastern trailhead is closed - please use detour.

Project Information

Contractor:

Strider

Construction Co., Inc.

Begin Construction:

April 13, 2015

Est. Completion Date:

October 2015

Project Description:

Relocate a mile of the road 300' inland, improve the two scenic vistas and the Mt. Finlayson's trail's eastern trailhead.



WASHINGTON STATE DEPARTMENT OF
Natural Resources



Contact Us:

cattlepointroad@dot.gov

Project Website:

<http://www.wfl.fhwa.dot.gov/projects/wa/cattlepoint/>

Project Engineer:

Don Brouillard
