

Suiattle River Road

MP 6.0 - MP 14.4 Combined Projects

CONSTRUCTION NEWSLETTER


August 23, 2013

Construction Begins

CONSTRUCTION ACTIVITIES

This week MidMountain Contractors began placing construction signs and gates while their subcontractors; Advanced Construction Surveyors began setting the clearing limits for the project and King Construction began mobilizing in their construction equipment.

Next week, MidMountain and their subcontractors will continue to mobilize in equipment, install erosion control devices, and on Wednesday, clearing is scheduled to begin.

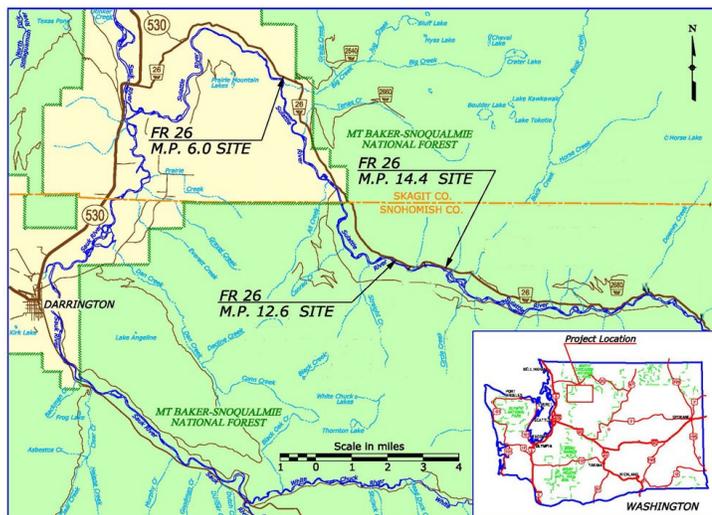

WORK SCHEDULE

Monday—Friday, 10 hours per day

DELAYS AND CLOSURES

August 28th, the road closure moves down to MP 11.6. The road will remain open to Pedestrian, Bicycle, Stock traffic as well as USFS administrative traffic.

September 6th, the road will be closed to all traffic due to the nature of the construction activities and will reopen to non-vehicular traffic on October 10th.

PLEASE USE CAUTION WHEN TRAVELLING THROUGH THE CONSTRUCTION ZONE.

Project Information

Contractor:

MidMountain
Contractors, Inc.

Begin Construction:

August 14, 2013

Est. Completion Date:

October 6, 2014

Project Description:

Project will repair the flood-damaged sites, abandon and rehabilitate other sections of road, reopening vehicle access to a variety National Forest recreation opportunities.



Contact Us: wfl.suiattleriverroad@dot.gov

Project Website: <http://www.wfl.fhwa.dot.gov/projects/wa/suiattle/>

Project Engineer:

Don Brouillard
