

# Cattle Point Road Relocation

## CONSTRUCTION NEWSLETTER

### Drainage Construction

August 7, 2015

#### CONSTRUCTION ACTIVITIES

This week Strider continued placing topsoil on the finished slopes and stabilized those slopes with mulch and tackifier. They installed utility vaults near the start of the project and began installing the conduits to those vaults. Culvert installation and rip rap culvert outlet protection were installed.

Next week, they will finish vault and conduit installation as well as the culvert installation and rip rap ditch construction. They plan on finishing portions of sub-grade and placing crushed rock to protect the finished grade.

Construction Zone speed limit is 20 mph. Please drive carefully.

The water truck will be working this weekend - Please drive carefully.

#### Project Information

**Contractor:**

Strider

Construction Co., Inc.

**Begin Construction:**

April 13, 2015

**Est. Completion Date:**

October 2015

**Project Description:**

Relocate a mile of the road 300' inland, improve the two scenic vistas and the Mt. Finlayson's trail's eastern trailhead.

Culvert Inlet construction\*




Installing rip rap outlet protection\*



Finishing ditches\*

\*Photos by Ben Fox, GeoTest, Inc.

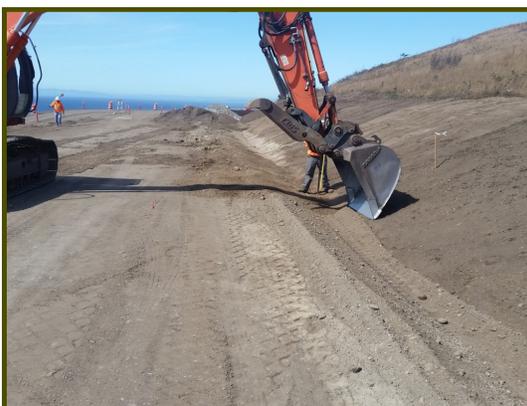

#### WORK SCHEDULE

Monday 8:00 - 6:00

Tue - Thu 7:00 - 6:00

Friday 7:00 - 2:30

#### DELAYS AND CLOSURES

**NPS and DNR Vistas are Closed.**

Delays: up to 15 min from 6 am to 8 am /  
up to 30 min from 8 am to 6 pm



WASHINGTON STATE DEPARTMENT OF  
**Natural Resources**



**Contact Us:** [cattlepointroad@dot.gov](mailto:cattlepointroad@dot.gov)

**Project Website:** <http://www.wfl.fhwa.dot.gov/projects/wa/cattlepoint/>

**Project Engineer:**  
Don Brouillard
