

Spruce Railroad Trail Segment C

CONSTRUCTION NEWSLETTER

January 20, 2017

Slope Stabilization Continues

CONSTRUCTION ACTIVITIES

Rock Dowel installation continued this week to secure the slope at the North Portal. To date, 34 dowels are installed and grouted, 28 more will be grouted today. Provided the performance testing goes well next week, the buttress material will be removed in a 2 stage process and additional dowels will be installed down to the level of the tunnel opening.


Drilling for Dowel Installation



Grouting the Dowel Bars



Working Late to get slope stabilization Completed

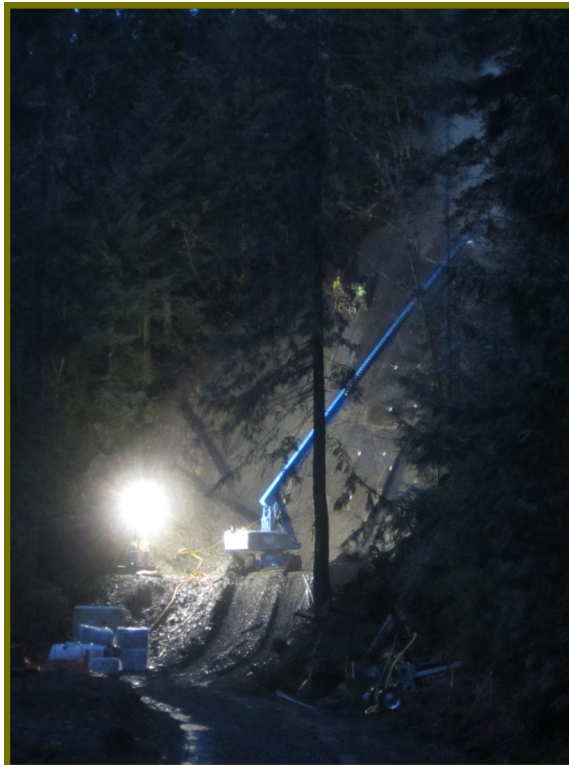

WORK SCHEDULE

Monday - Saturday, 7 am - 6 pm

DELAYS AND CLOSURES

The Olympic Discovery Trail is closed from the ONP Trailhead near the Lyre River to the paved trail section near Camp David Jr. Due to Rockfall Dangers there is NO access to Devil's Punchbowl.

Project Information

Contractor:

Bruch & Bruch

Construction, Inc.

Begin Construction:

September 19, 2016

Est. Completion Date:

May, 2017

Project Description:

This project will reopen a 1/2 mile segment of the Spruce Railroad Trail which includes refurbishing a 450' tunnel and the trailhead parking area.



Contact Us:

donald.brouillard@dot.gov

Project Website:

<https://flh.fhwa.dot.gov/projects/wa/Spruce-C>

Project Engineer:

Don Brouillard
